GO Expansion

Kitchener Fourth Track and Bloor Station (TTC Connection) Construction Liaison Committee

Thursday, September 12th 2024





AGENDA

- Welcome & Introductions
- Land Acknowledgment
- Safety Moment
- GO Expansion Overview
- Kitchener Fourth Track
 - Project Overview
 - Project Timeline
 - Work Progress
 - What To Expect Next

- Bloor TTC Connection
 - Project Overview
 - Project Timeline
 - Work Progress
 - What To Expect Next
- Committee Discussion
- Community Engagement

Land Acknowledgement

LAND ACKNOWLEDGEMENT

Let us take a moment to acknowledge we are on lands that have been, and continue to be, home to many Indigenous Peoples including the Anishnabeg, the Haudenosaunee and the Huron-Wendat peoples.

We are all Treaty people. Many of us have come here as settlers, as immigrants or involuntarily as part of the trans-Atlantic slave trade, in this generation, or generations past.

We acknowledge the historic and continued impacts of colonization and the need to work towards meaningful reconciliation with the original caretakers of this land.



We acknowledge that Metrolinx operates on territories and lands covered by many treaties that affirm and value the rights of Indigenous communities, Nations and Peoples.


We understand the importance of working towards reconciliation with the original caretakers of this land. At Metrolinx, we will conduct business in a manner that is built on a foundation of trust, respect and collaboration.



Safety Moment


GO Expansion Overview

The GO Expansion program will provide a range of improvements across the GTHA:

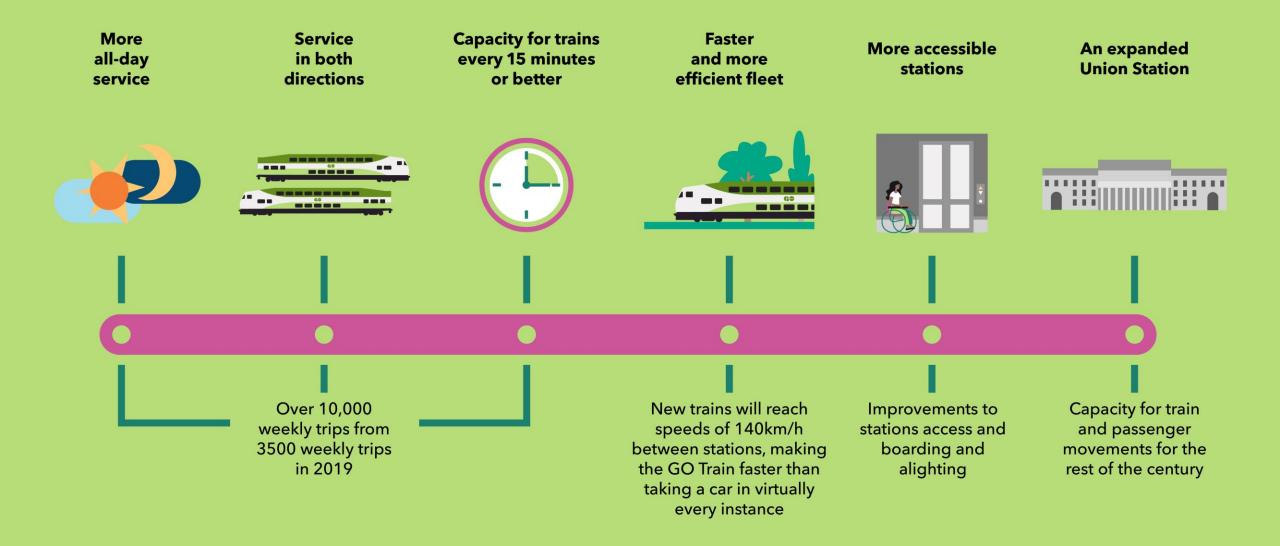



GO Expansion

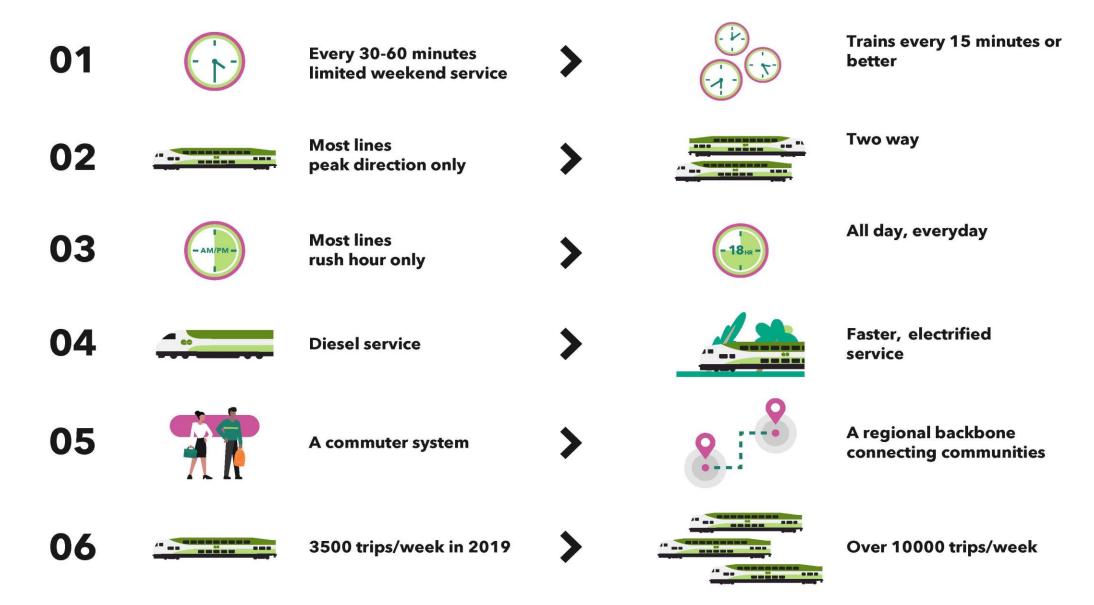


WHAT ARE WE DOING

Metrolinx GO Expansion Program

Metrolinx is working to transform the way the region moves by building a seamless, convenient and integrated transit network across the Greater Golden Horseshoe. Over the next 10 years, Metrolinx is transforming the existing GO rail system to deliver a whole new rapid transit experience to your community. With more frequent train service you will have more options to get where you need to go.

Kitchener GO Line Expansion

The Kitchener Fourth Track project is a segment of work that is a part of the overall GO Expansion program. The realignment of the West Toronto Railpath will facilitate the new track to be installed and allow for more trains to be added to the Kitchener line. The Kitchener GO Line Expansion will bring all-day, two-way GO service for people across Toronto, Brampton and Kitchener.



->>> METROLINX

Kitchener Fourth Track Project Overview

Project timeline

Activity	2024			2025		
	Summer	Fall	Winter	Spring	Summer	Fall
Tunnel Construction						
Track Work						
Noise Wall Installation						
WTRP Dupont to Wallace						
WTRP Bloor to Dundas						
Ernest Ave Park						
WTRP Wallace to Bloor						

This timeline may be subject to change due to weather or unforeseen circumstances

COMPLETED

Ernest Ave Park

- Excavation and grading
- Concrete and asphalt paving
- New topsoil and trees
- Irrigation lines




Ernest Ave Park

- Shrub planting
- Vine wall cable system
- Decorative fencing
- Lighting




Bloor GO

- Tunnel roof formwork and pour
- Electrical and Mechanical Work

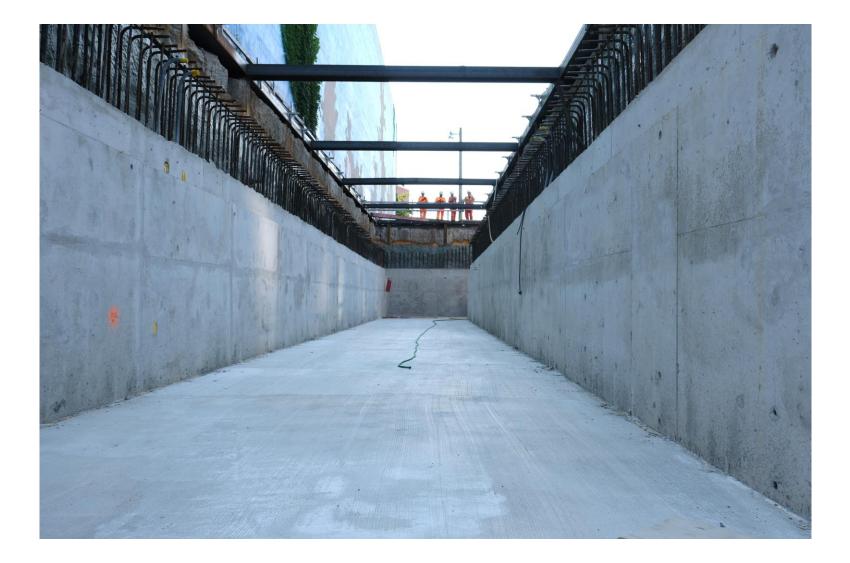

Bloor St Bridge Work

- 1 Week sidewalk closure under the bridge in early October
- Installation of remaining cover plates and brackets.

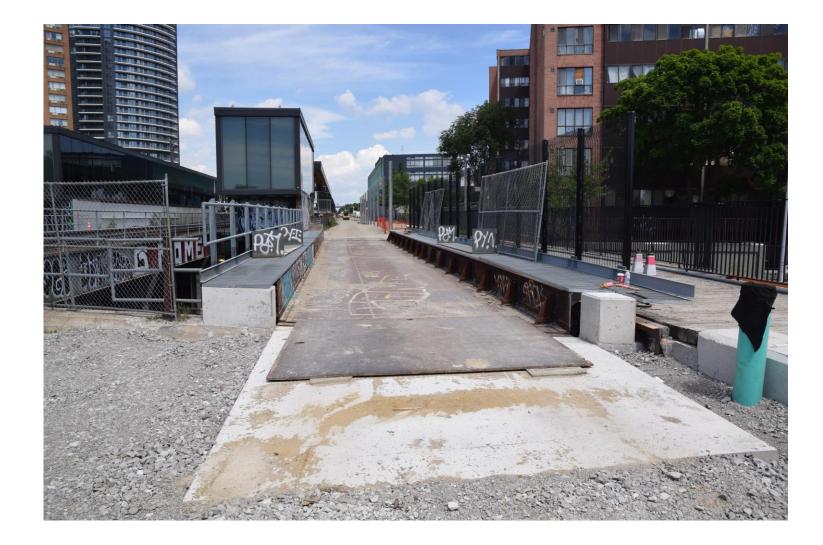

WHAT TO EXPECT NEXT

Concrete Paving

• Perth Ave connection to the Railpath




Bloor TTC Connection Project Overview

COMPLETED

Shoring wall for the Pedestrian Box structure – Stage 2


• Shoring wall stage 2 has been completed.

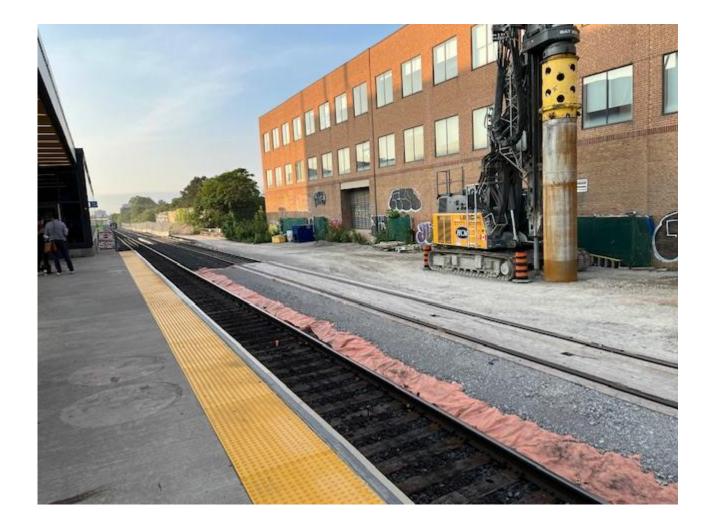

COMPLETED

CN/Bell 360 line relocation - Phase 2

 Relocation of the CN and Bell 360 line away from the future Pedestrian box structure has been completed. The cables are currently installed in between tracks and shoring wall

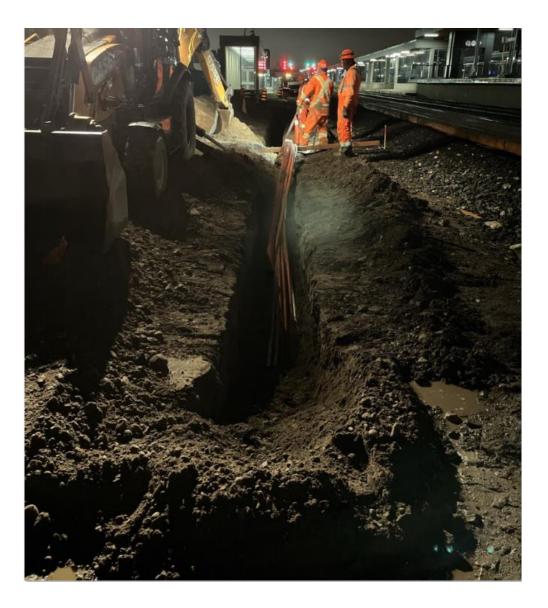


Jet Grouting

• Commence Jet Grouting at the Pedestrian Box structure



Renovation and repairs inside the Crossways building

• Repairs inside the Crossways building at P1 as well as P2 level is continuing.

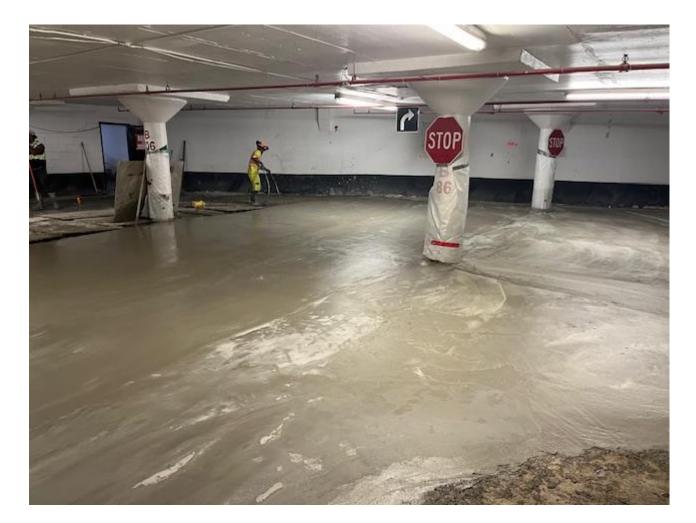

WHAT TO EXPECT NEXT

The Pedestrian box structure Construction

- Excavation
- Waterproofing

Work schedule

• Work scheduled to occur overnight from Sunday to Thursday, from 8 p.m. to 5 a.m. (5 nights a week).

Community Impacts: Noise, Dust and Light.

 Noise and air monitors have been installed around the project area to ensure that the project requirements are met. Any exceedances will be flagged & mitigated, wherever possible.




WHAT TO EXPECT NEXT

Excavation for Stairs and elevators inside the Crossways Building

 Stairs and Elevators openings and excavation scheduled to occur during the day, Monday to Friday, from 7a.m. to 4p.m.

Community Impacts: Noise

- The dust from the excavation will be contained inside the hoarded area.
- There will be some noise impact to the businesses close to the work area

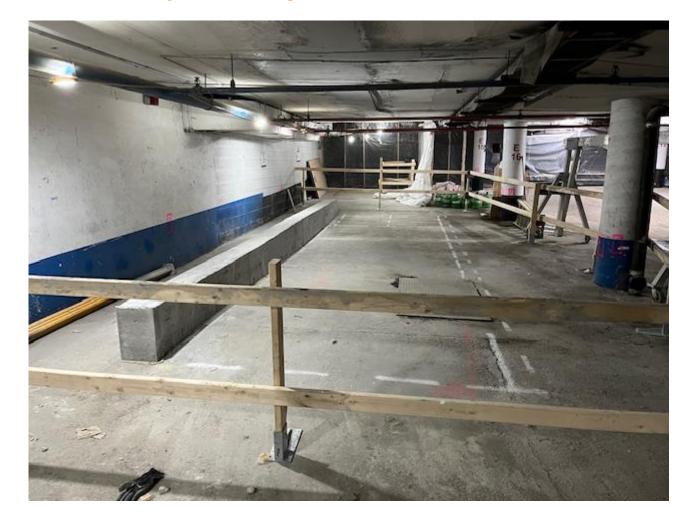

Committee Discussion

Community Engagement

COMMUNITY ENGAGEMENT

Updates will be communicated to the community

- via: Canada Post Mail Drops
 - Weekly Toronto West e-newsletter
 - Project Website (metrolinx.com/kitchener)
 - Upcoming Virtual & In-Person Public Meetings
 - Upcoming Community Pop-ups
 - Toronto West phone number: 416-202-6911
 - Toronto West email: <u>TorontoWest@metrolinx.com</u>
 - X: @GOExpansion
 - Metrolinx Engage
 - Next scheduled CLC: Thursday, October 10th

Cet présentation est disponible en français sur demande. Si vous êtes intéressé, veuillez envoyer un courriel à <u>TorontoWest@metrolinx.com</u>

##
