


# Don Yard Rail Corridor Bi-Weekly Construction Update

Monday March 3 to Friday March 14, 2025

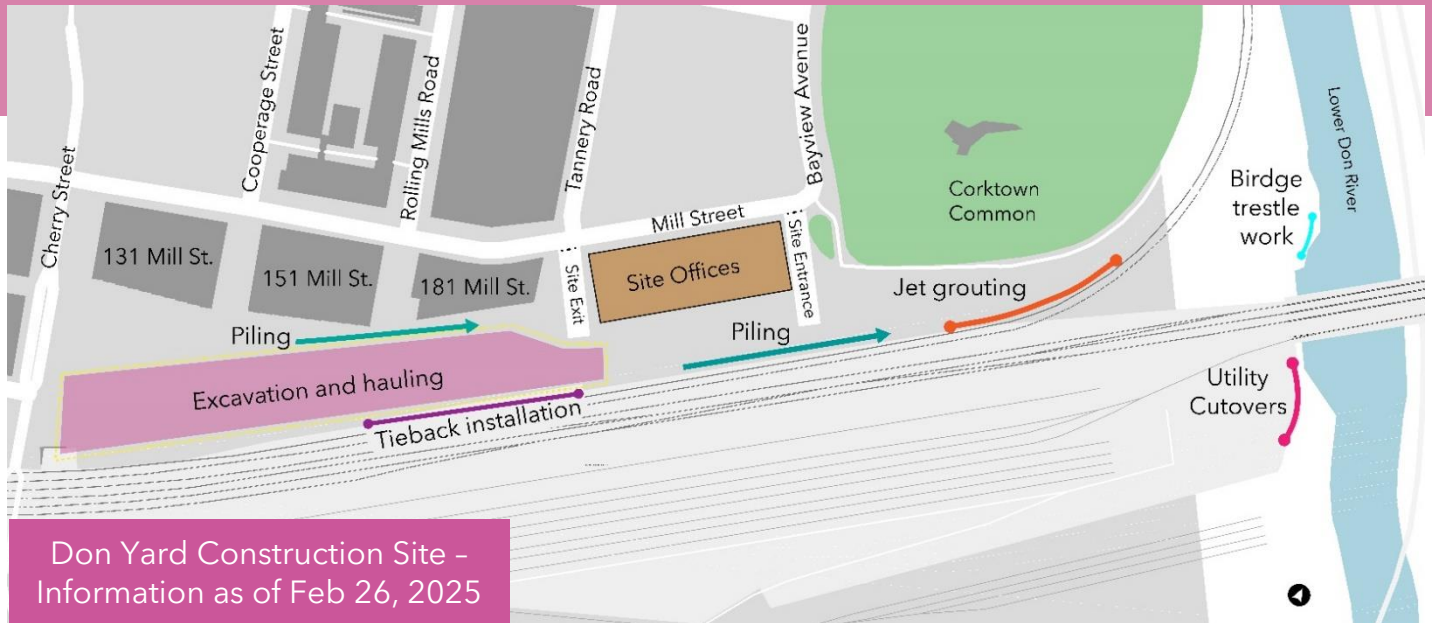

Don Yard Construction Site - Information as of Feb 26, 2025

**This notice provides an update on the work happening in the Don Yard rail corridor over the next two (2) weeks. The notice will be updated on a bi-weekly basis.**

### What is happening?

Construction work is underway in the Don Yard rail corridor to prepare for the future Ontario Line. A new subway tunnel and portal are being built in the Don Yard to transition the Ontario Line from underground to surface level. There will also be a new bridge constructed over the Don Valley Parkway. This notice provides a progress update on the works taking place in the Don Yard. **For further details, please carefully review the information provided in the table below.**

Hours of Work and Duration	Location	Activity
<p><b>Monday March 3 to Monday March 10, 2025</b>  <b>Overnight</b></p> <ul style="list-style-type: none"> <li>Weekdays and weekends from 10 p.m. - 5 a.m.</li> </ul>	<ul style="list-style-type: none"> <li>East end of the site, beside the Lower Don River</li> </ul>	<p><b>Utility Cutovers</b></p> <p>Moving high voltage utility cables over onto a new hydro-one transmission tower. For safety, work needs to be done at night when trains are not operating.</p>
<p><b>Ongoing until April 2025</b>  <b>Daytime and overnight</b></p> <ul style="list-style-type: none"> <li>Weekdays 7 a.m. - 2 a.m.</li> <li>Saturdays from 7 a.m. - 5 p.m.</li> </ul>	<ul style="list-style-type: none"> <li>West end of the site, near Cherry Street</li> <li>Middle of the site, near the site offices (piling in this area can only occur when trains are not running and therefore must take place until 5 a.m. Work in this area will be completed in mid-March)</li> </ul>	<p><b>Piling</b></p> <p>Using a drill rig to dig circular holes in the ground. These holes are then filled with rebar and concrete to create a wall that will support the tunnel excavation. Piling is progressing west to east.</p>
<p><b>Ongoing until July 2025</b>  <b>Daytime and overnight</b></p> <ul style="list-style-type: none"> <li>Monday to Sunday, 24 hrs.</li> </ul>	<ul style="list-style-type: none"> <li>East end of the site, south of Corktown Common</li> </ul>	<p><b>Jet Grouting</b></p> <p>Using a small drill to inject grout into the ground. The grout helps to stabilize the ground and improve soil conditions.</p>
<p><b>Ongoing until September 2025</b>  <b>Daytime</b></p> <ul style="list-style-type: none"> <li>Weekdays and Saturdays from 7 a.m. - 5 p.m.</li> </ul>	<ul style="list-style-type: none"> <li>Middle of the site, south of 131 - 181 Mill Street</li> </ul>	<p><b>Excavation, hauling and tieback installation</b></p> <p>Using excavators and dump trucks to remove material (soil) from the site. Using a drill to install steel rods that will support the excavation. Activities progress west to east.</p>
<p><b>Ongoing until December 2025</b>  <b>Daytime</b></p> <ul style="list-style-type: none"> <li>Weekdays 7 a.m. - 5 p.m.</li> </ul>	<ul style="list-style-type: none"> <li>At the east end of the site, beside the Don River</li> </ul>	<p><b>Bridge trestle work</b></p> <p>Installing foundations for the temporary bridge. Construction activities include excavation and concrete works.</p>

\*Work locations may change based on construction progress and site conditions.
