


Don Yard Rail Corridor Bi-Weekly Construction Update

Monday April 21 to Friday, May 2, 2025

This notice provides an update on the work happening in the Don Yard rail corridor over the next two (2) weeks. The notice will be updated on a bi-weekly basis.

No work over the Easter long weekend (work resumes Monday, April 21, 2025)

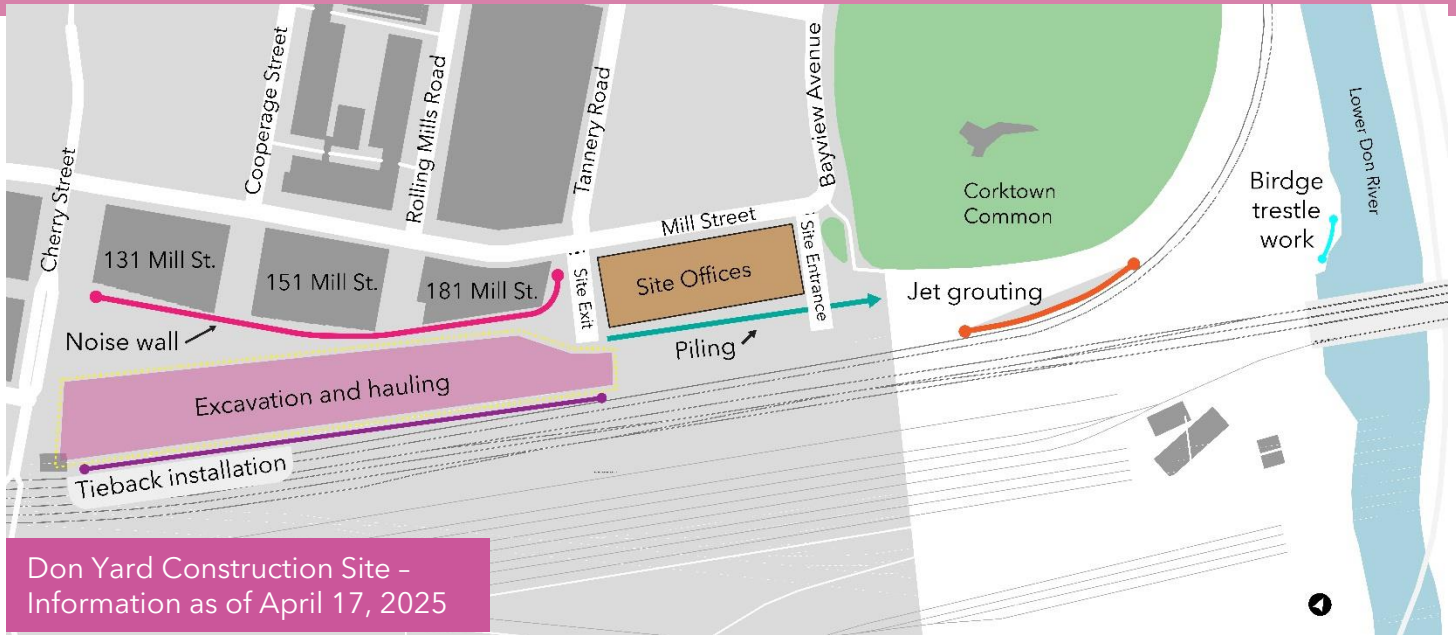

What is happening?

Construction work is underway in the Don Yard rail corridor to prepare for the future Ontario Line. A new subway tunnel and portal are being built in the Don Yard to transition the Ontario Line from underground to surface level. There will also be a new bridge constructed over the Don Valley Parkway. This notice provides a progress update on the works taking place in the Don Yard. **For further details, please carefully review the information provided in the table below.**

Hours of Work and Duration	Location	Activity
<p>Ongoing until May 2025 Daytime and overnight</p> <ul style="list-style-type: none"> Weekdays 7 a.m. - 2 a.m. 	<ul style="list-style-type: none"> Middle of the site from the east end of 181 Mill Street towards Bayview Avenue 	<p>Piling</p> <p>Using a drill rig to dig circular holes in the ground. These holes are then filled with steel and concrete to create a wall that will support the tunnel excavation. Piling is progressing west to east.</p>
<p>Ongoing until July 2025 Daytime and overnight</p> <ul style="list-style-type: none"> Monday to Saturday, 24 hrs. 	<ul style="list-style-type: none"> East end of the site, south of Corktown Common 	<p>Jet Grouting</p> <p>Using a small drill to inject grout into the ground. The grout helps to stabilize the ground and improve soil conditions.</p>
<p>Ongoing until December 2025 Daytime</p> <ul style="list-style-type: none"> Weekdays and Saturdays from 7 a.m. - 5 p.m. <u>Intermittent overnight excavation work will resume as early as April 28 (earliest)</u> 	<ul style="list-style-type: none"> Middle of the site, south of 131, 151, and 181 Mill Street 	<p>Excavation, hauling and tieback installation</p> <p>Using excavators and dump trucks to remove material (soil) from the site. Using a drill to install steel rods that will support excavation. Activities progress west to east.</p>
<p>Ongoing until December 2025 Daytime</p> <ul style="list-style-type: none"> Weekdays and Saturdays 7 a.m. - 5 p.m. 	<ul style="list-style-type: none"> At the east end of the site, beside the Don River 	<p>Bridge trestle work</p> <p>Installing foundations for the temporary bridge. Construction activities include excavation and concrete works.</p>
<p>Ongoing until early May 2025 Daytime</p> <ul style="list-style-type: none"> Weekdays 7 a.m. - 5 p.m. 	<ul style="list-style-type: none"> South of 131, 151 and 181 Mill Street (Maple House) 	<p>Noise wall installation</p> <p>Installing a 5-metre-tall noise wall along the north side of the site from Cherry Street to the site entrance (in front of Maple House).</p>

*Work locations may change based on construction progress and site conditions.
