

GO Expansion

Kitchener Fourth Track and Bloor Station (TTC Connection) Construction Liaison Committee

June 12, 2025



AGENDA

- Land Acknowledgment
 - Safety Moment
 - GO Expansion Overview
 - Kitchener Fourth Track
 - Project Overview
 - Project Timeline
 - Work Progress
 - What To Expect Next
 - Bloor TTC Connection
 - Project Overview
 - Project Timeline
 - Work Progress
 - What To Expect Next
 - Committee Discussion
 - Community Engagement
-

LAND ACKNOWLEDGEMENT

Metrolinx acknowledges that we connect communities by building and operating transit within the traditional lands of the Anishinaabe, the Haudenosaunee and the Huron-Wendat peoples, for whom these lands continue to have great importance.

Treaties between First Nations and governments cover these lands, and the promises contained in these Treaties remain relevant to this day.

Metrolinx and its employees are committed to understanding the history of these lands and the continued impacts of colonization and take responsibility for actions to advance reconciliation.

Metrolinx will continue to seek the knowledge, expertise and experience of Indigenous partners and commits to doing business in a manner that is built on a foundation of trust, respect and collaboration.



Safety Moment

GO Expansion Overview

The GO Expansion program will provide a range of improvements across the GTHA:

**More
all-day
service**



**Service
in both
directions**



**Capacity for trains
every 15 minutes
or better**



**Faster
and more
efficient fleet**



**More accessible
stations**



**An expanded
Union Station**



Over 10,000
weekly trips from
3500 weekly trips
in 2019


New trains will reach
speeds of 140km/h
between stations, making
the GO Train faster than
taking a car in virtually
every instance

Improvements to
stations access and
boarding and
alighting

Capacity for train
and passenger
movements for the
rest of the century

Kitchener Fourth Track Project Update

Project Timeline

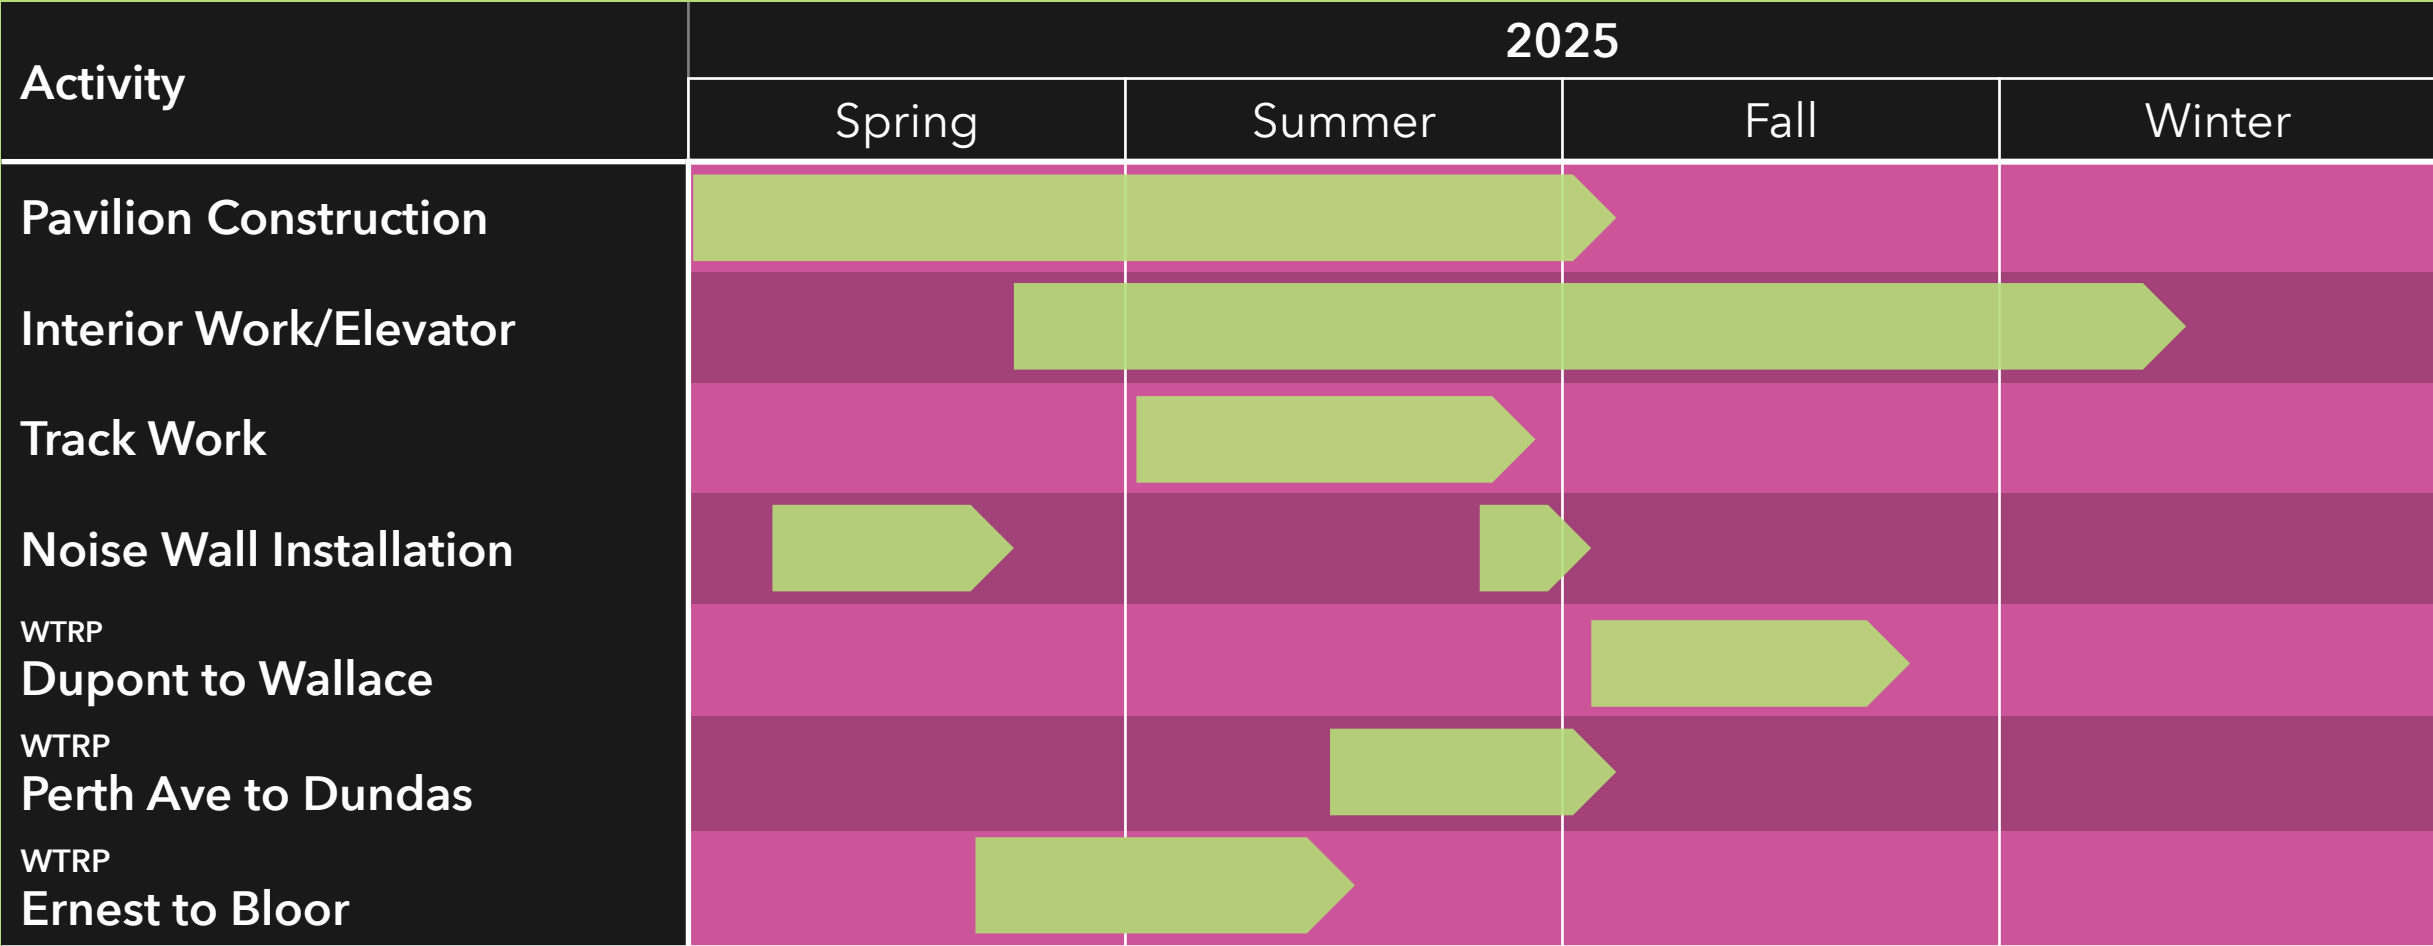

This timeline may be subject to change due to weather or unforeseen circumstances

COMPLETED

Noise Wall Installation

- North of Bloor Street



IN PROGRESS

Track Installation


- Ballast
- Rail welding



IN PROGRESS

Bloor GO Tie Bracing

- Installation of support brackets to ensure track is at the correct height and distance from platforms
- Work is being done with hand tools

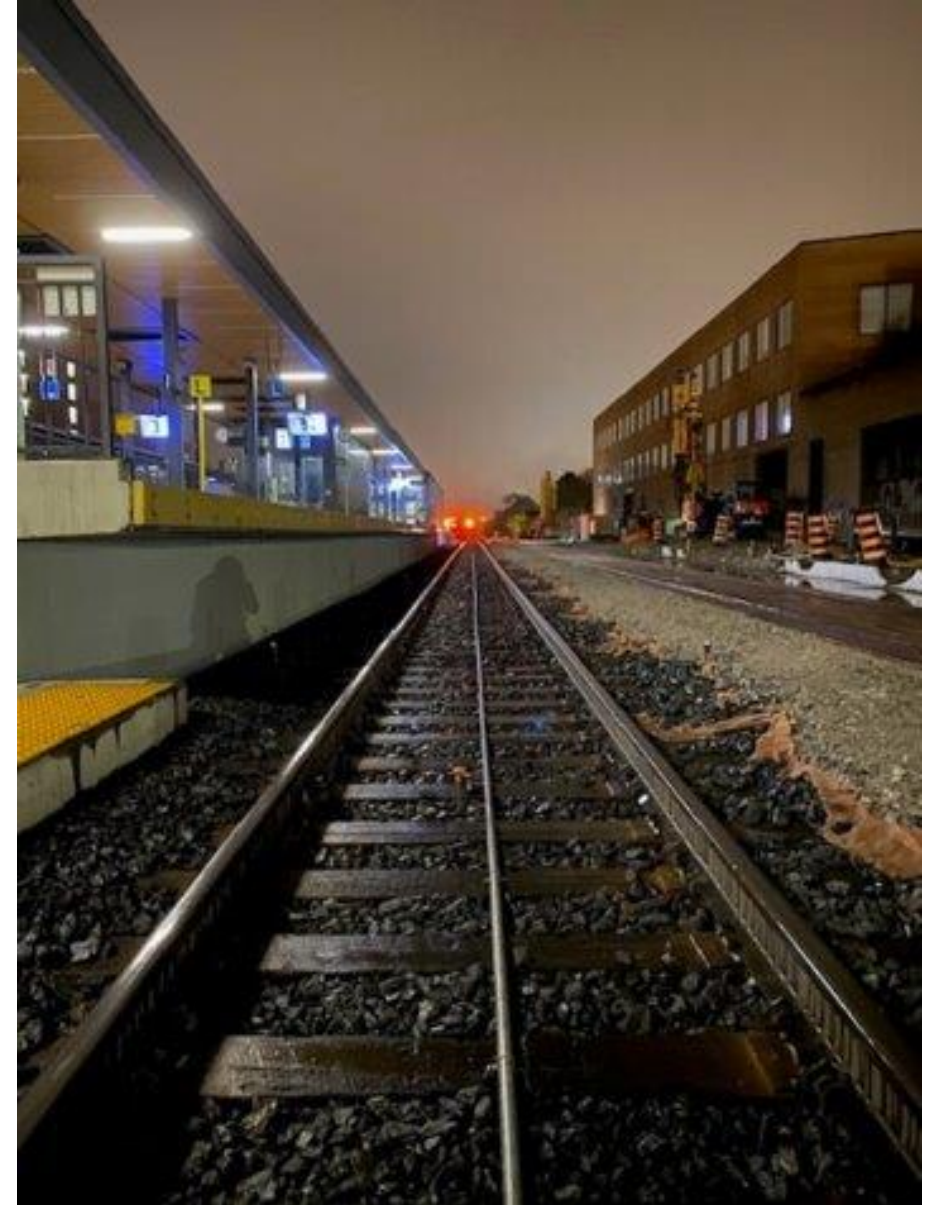

IN PROGRESS

Tunnel Electrical and Interior Work


- Doors and frames
- Painting
- Electrical panel
- Drywall
- Concrete finishing



IN PROGRESS

Railpath Realignment (North of Bloor Street)

- Trench drain installation
- Grading and concrete work

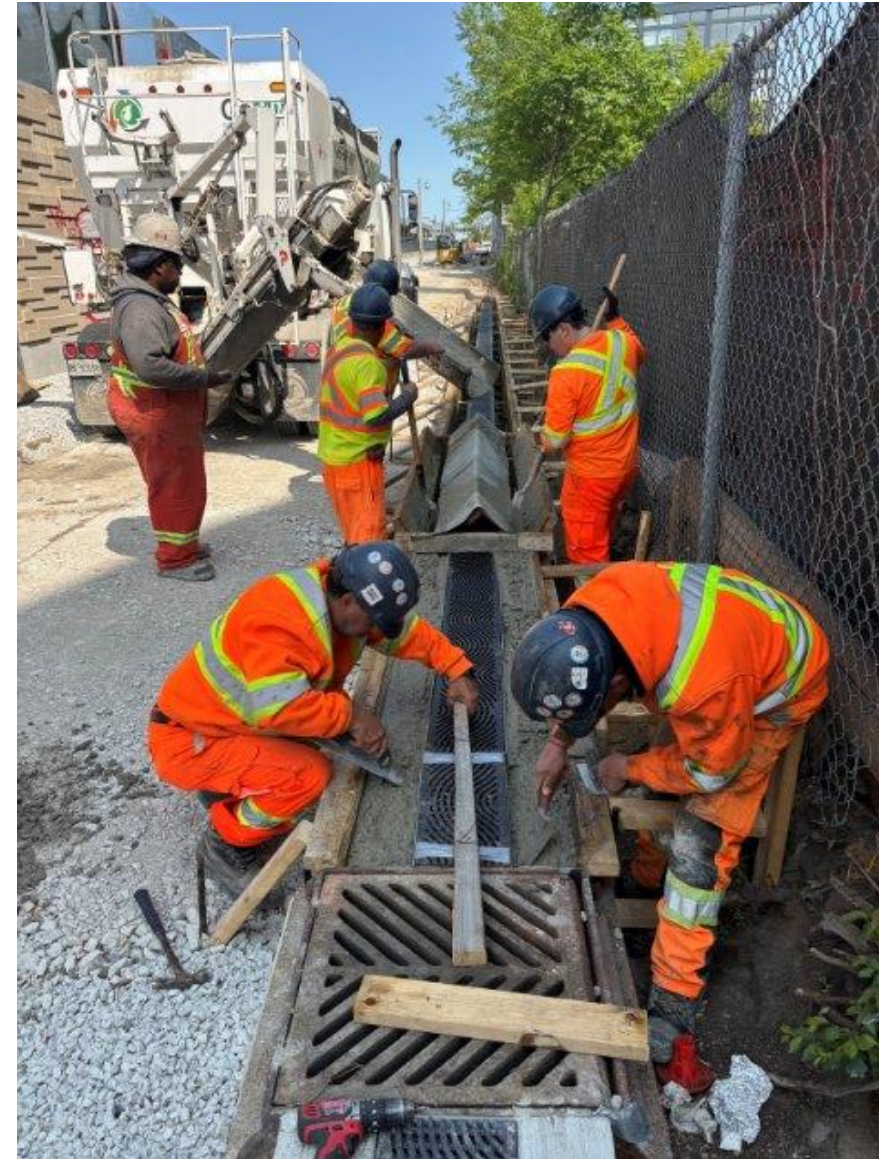

WHAT TO EXPECT NEXT

Bloor GO Tunnel/Pavillion

- Painting
- Roof deck and waterproofing
- Kneewall cladding installation
- elevator



WHAT TO EXPECT NEXT

Track Work

- Dupont Street to Wallace Avenue
- Rail and tie layout



WHAT TO EXPECT NEXT

Drainage and Ditching

- Dundas Street West to Lansdowne Avenue
- Soakaway pit installation



Bloor TTC Connection Project Update

PROJECT TIMELINE


Activity	2024	2025				2026	
	Fall	Winter	Spring	Summer	Fall	Winter	Spring
New Pedestrian Box Structure							
Crossway Building works							
TTC Station Works							

This timeline may be subject to change due to weather or unforeseen circumstances

IN PROGRESS

Jet Grouting

- At the Pedestrian Box structure

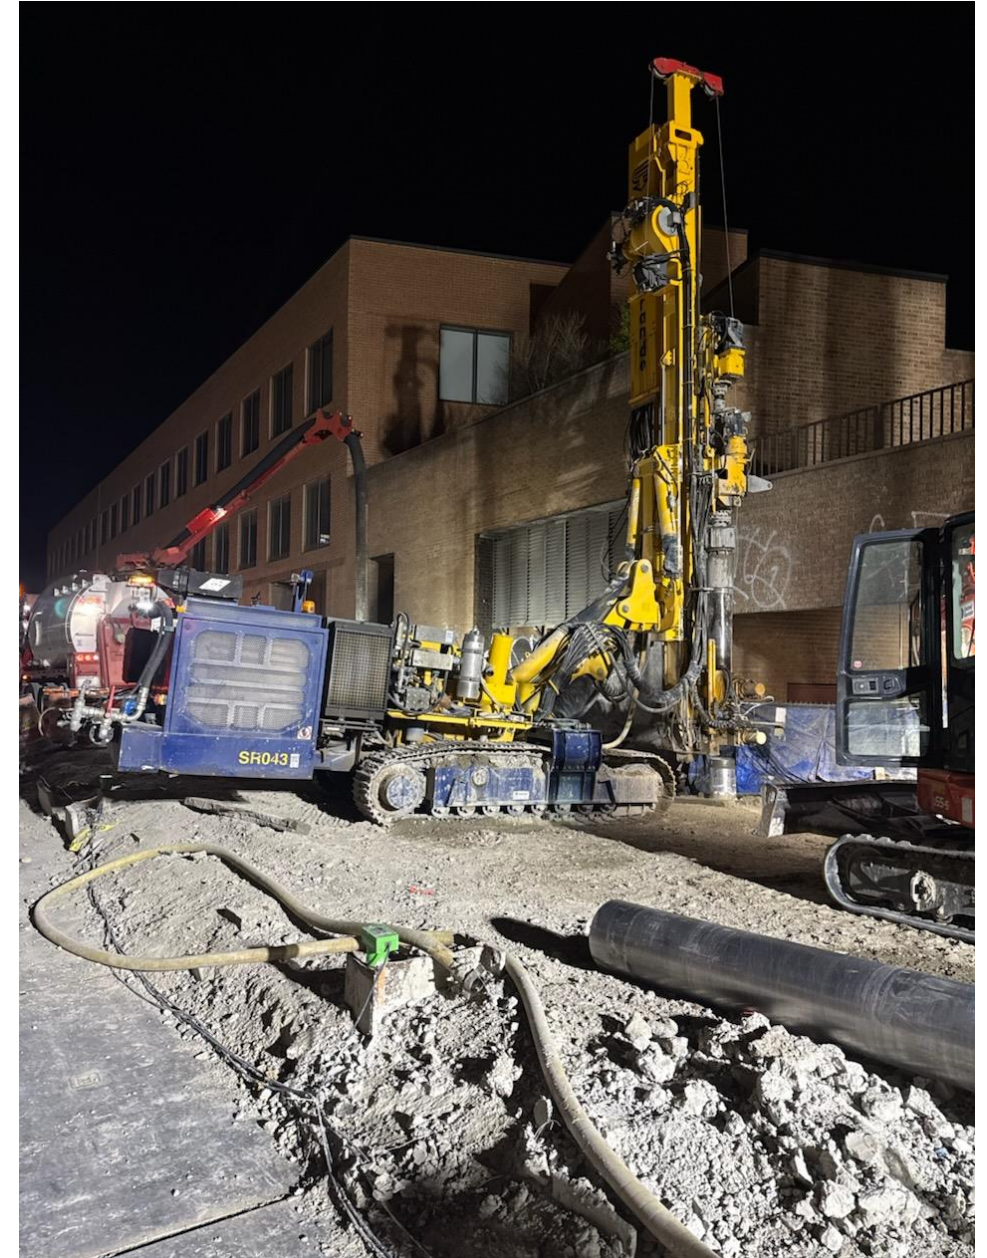

IN PROGRESS

Localized Subgrade Injections


- Localized Subgrade Injections within the P2 level of the Crossways Complex

Work Schedule

- Work is scheduled to occur during the day, Monday to Friday, from 7 a.m. to 4 p.m.

Community Impacts

- No impact to community as work is being completed within the hoarded area.

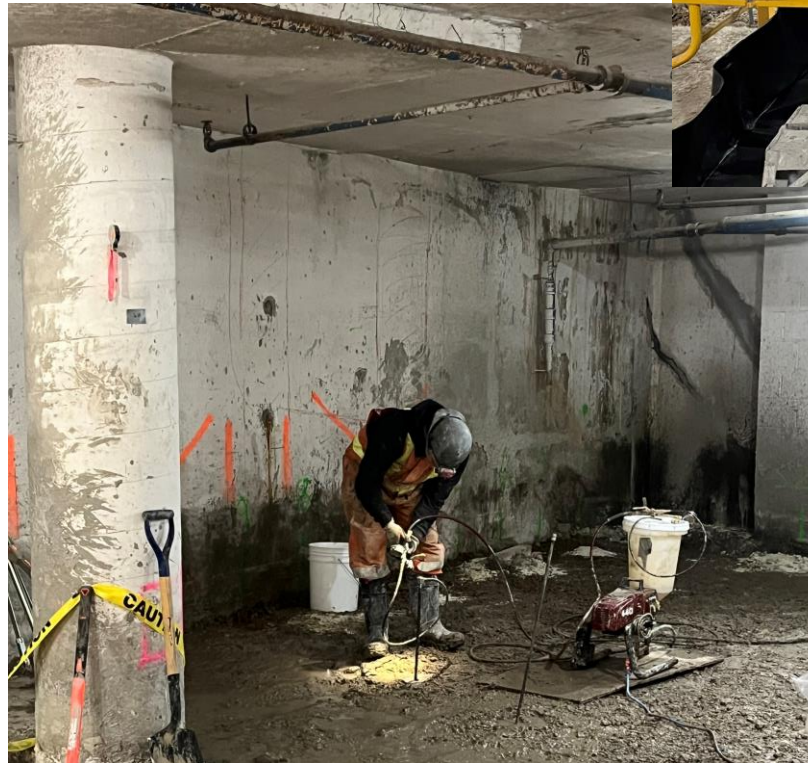

IN PROGRESS

Monitoring Wells

- Decommissioning of monitoring wells within the laydown area.

Work Schedule

- The decommissioning is scheduled to occur during the day, from 9am to 12pm.

Community Impacts

- No impact to community as work is being completed within the hoarded area.



IN PROGRESS

Bus Duct Relocation P2 level

- Installing Bus Duct Cables within the Crossways P2 - Laundry and Storage Room

Work Schedule

- Cable Install is scheduled to occur during the night, Monday to Friday, from 12 a.m. to 8 a.m.

Community Impacts

- No impact to community as work is being completed in off peak hours.



WHAT TO EXPECT NEXT

Generator Installation Bloor GO PPUDO

Work schedule

- Generator Delivery is scheduled to occur during off peak hours

Community Impacts:

- All work will be within the hoarded area. Traffic Control will be implemented, and proper signage will be displayed for the duration of the work.



WHAT TO EXPECT NEXT

Staircase B and C Removals

- Cutting and removals of Staircase B and C Slab within Crossways P2

Work schedule

- Removals are scheduled to occur, Monday to Friday, during the day, from 7 a.m. to 4 p.m.

Community Impacts:

- Noise and air monitors have been installed around the project area to ensure that the project requirements are met
- Any exceedances will be flagged and mitigated, wherever possible.



WHAT TO EXPECT NEXT

The Pedestrian box structure construction

- Excavation
- Waterproofing

Work schedule

- Work scheduled to occur overnight from Sunday to Thursday, from 8 p.m. to 5 a.m. (5 nights a week).

Community Impacts: Noise, Dust and Light

- Noise and air monitors have been installed around the project area to ensure that the project requirements are met. Any exceedances will be flagged & mitigated, wherever possible.



Committee Discussion

COMMUNITY ENGAGEMENT

Updates will be communicated to the community via:

- Canada Post Mail Drops
- Bi-weekly Toronto West e-newsletter
- Project Website (metrolinx.com/kitchener)
- Monthly Construction Liaison Committee (CLC) meeting
- Virtual and In-Person Public Meetings
- Community Pop-ups
- Toronto West Phone Number: 416-202-6911
- Toronto West email: TorontoWest@metrolinx.com
- X: @GOExpansion
- Metrolinx Engage

Cette présentation est disponible en français sur demande. Si vous êtes intéressé, veuillez envoyer un courriel à TorontoWest@metrolinx.com

