



# Lakeshore East West Corridor

## Expansion: Early Work - Package B

Construction Liaison Committee Meeting

More info: [metrolinx.com/lakeshoreeastrailcorridor/](https://metrolinx.com/lakeshoreeastrailcorridor/)  
Contact: [TorontoEast@Metrolinx.com](mailto:TorontoEast@Metrolinx.com)

July 5, 2023

# Land Acknowledgment

Let us take a moment to acknowledge we are on lands that have been, and continue to be, home to many Indigenous Peoples including the Anishnabeg, the Haudenosaunee and the Huron-Wendat peoples.

We are all Treaty people. Many of us have come here as settlers, as immigrants or involuntarily as part of the trans-Atlantic slave trade, in this generation, or generations past.

We acknowledge the historic and continued impacts of colonization and the need to work towards meaningful reconciliation with the original caretakers of this land.

We acknowledge that Metrolinx operates on territories and lands covered by many treaties that affirm and value the rights of Indigenous communities, Nations and Peoples.

We understand the importance of working towards reconciliation with the original caretakers of this land. At Metrolinx, we will conduct business in a manner that is built on a foundation of trust, respect and collaboration.

# Terms of Reference

The CLC will provide a communication forum for the Lakeshore East-West (Package B) construction project team and community representatives of area residents and businesses to proactively and regularly communicate and discuss construction activities and community impacts. The committee is designed to enable regular access to construction-related information, including schedule and timing information for local business owners, community groups and residents, through CLC representatives and discussions.

## The Lakeshore East-West Team will:

- Provide accurate, understandable and timely information.
- Be open to feedback, give careful consideration to ideas, and report back to the larger project team.
- Adhere to all aspects of the Terms of Reference and Code of Conduct.

## Community Representatives or Area Residents and Businesses will:

- Participate actively in regular meetings.
- Be open and receptive to ideas.
- Liaise and act as a representative of pre-identified organization/community/business or stakeholder group by providing feedback to the project team and formally communicating relevant information back to their respective groups.
- Adhere to all aspects of the Terms of Reference and Code of Conduct.

# Safety Moment

## Insect Bites

### Overview

When working outside, you can be exposed to bites and stings. Some examples of insects that you may come across include:

- Ants
- Stinging flying insects such as bees, wasps, and hornets
- Ticks
- Spiders
- Mosquitoes
- Flies

### Symptoms of Insect Bites and Stings

- West Nile Virus - Headache, stiff neck, fever, nausea, vomiting, drowsiness, confusion
- Lyme Disease - Fever, chills, fatigue, muscle and/or joint pain, distinct bullseye rash



- Allergic Reactions - Swelling in the face/neck, or wherever stung, difficulty breathing, drop in blood pressure, dizziness

### Protect Yourself

- Routinely check your body for ticks.
- If you spot a tick, remove it as soon as possible:
  - With fine-tipped tweezers, gently grasp the tick and pull it in an upwards direction, away from your skin.
- TIP: ticks can be brought to local public health unit to be tested for Lyme disease
- Wear insect repellent when you know you are going to be working outside. Products containing 20-30% DEET have been shown to provide several hours of protection.
- Long-sleeve shirts and pants provide superior protection when working outside.

## Slide 4

---

**CW0**

Safety moment to be updated ahead of the meeting

Charlene Watt, 2023-06-14T14:22:48.123

# Project Update – Package B

## Action Items

July 2023

# July Construction Complaints CW0

Complaint	Action
Noise at Warden and Danforth Bridges	Received complaints about the overnight noise at Warden and Danforth Bridges and inquiries about how long it would last. Work at the bridges is expected to be ongoing until Summer 2024, and the current piling work will continue for the next several months.

## Slide 6

---

**CW0**

Latest complaints to be added ahead of the meeting

Charlene Watt, 2023-06-14T14:33:55.256



## July CLC Action Items

There were no action items from the June CLC Meeting.

## July Noise Exceedances CW0

There were no construction-related vibration exceedances in June, however there were a few instances of noise exceedances related to the ongoing work at Danforth and Warden Bridges.

## Slide 7

---

**CW0** Exceedance data to be confirmed, and slide updated, ahead of the meeting  
Charlene Watt, 2023-06-14T14:26:46.289


# Project Update – Package B

## Woodbine Avenue to Warden Avenue

LS Lakeshore Constructors


July 2023

# PROJECT CONSTRUCTION MILESTONES

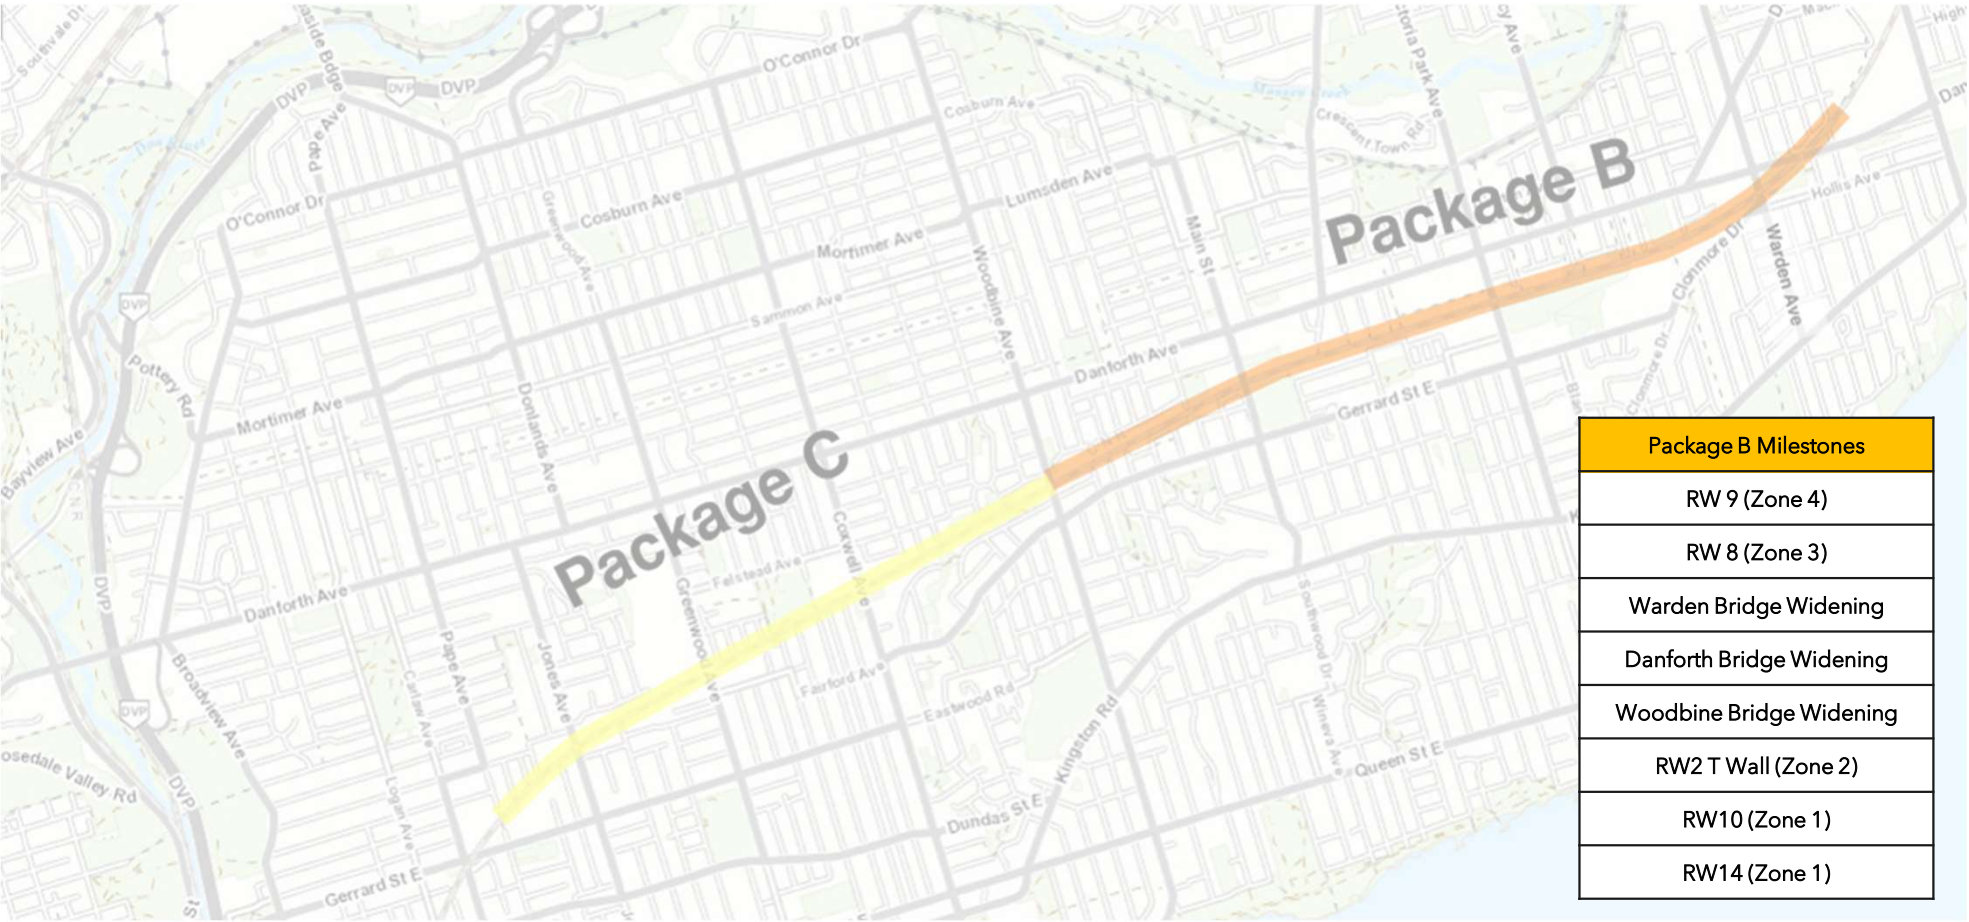

## Wolcott Ave. to Warden Ave. CW0

- The partial road closure at Kimridge Ave. will be leveraged on an as-needed basis
- Both the north and south lanes of Kimridge Ave. will remain open to traffic, though the lanes will be narrowed in this area

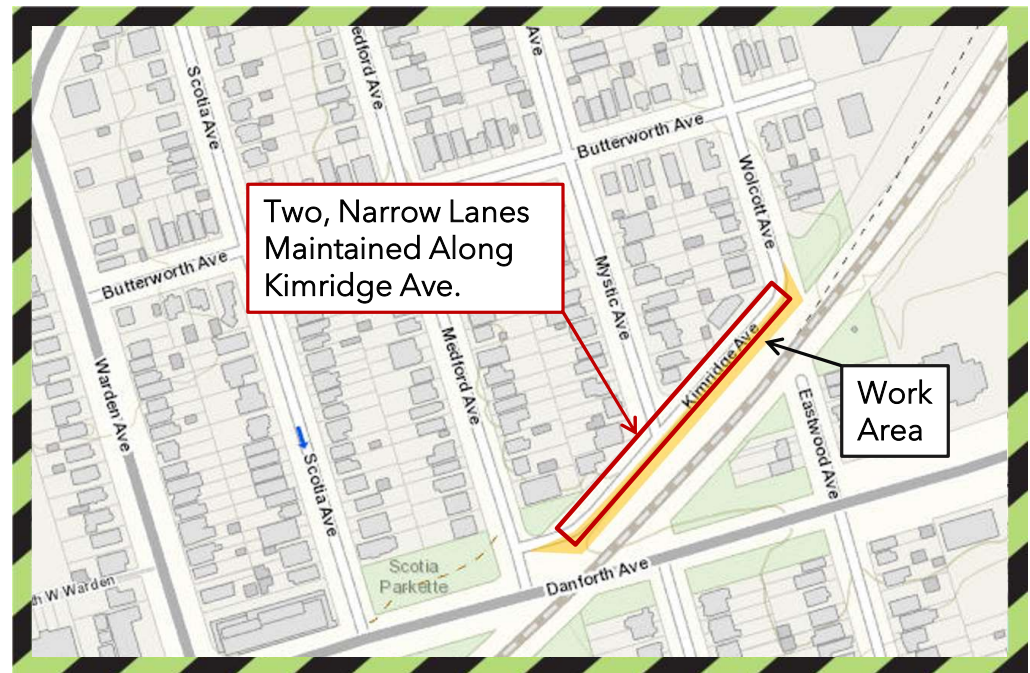

## Slide 10

---

**CW0** Get an updated timeline for RW10 from Tariq ahead of meeting  
Charlene Watt, 2023-06-14T15:10:26.210

## Warden Ave. to Victoria Park Ave.


- Grading and stripping work is underway to prepare the area for the raceway installation.
- Grading and stripping work is underway to prepare the area for the RW 2 pad.
- Duration: ~ 4 months
- Day & Night Shift





## Victoria Park Ave. to Main St. (South Side of the Corridor)

- Installation of the soakaway (drainage measure) is ongoing
- Final grading and sub-ballast installation to follow
- Duration: ~ 4 months
- Day & Night Shift

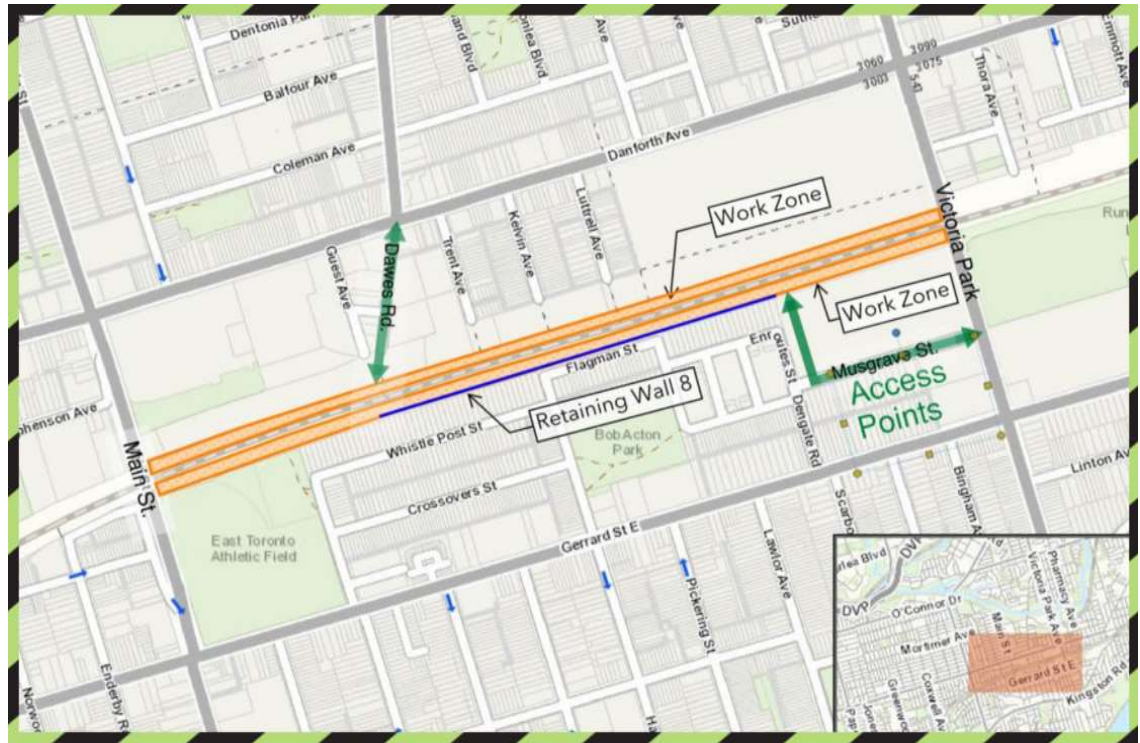




## Main St. to Woodbine Ave. (North Side of the Corridor)

- The raceway installation is underway
- Installation of the soakaway (drainage measure) and final grading are to follow.
- Duration: ~ 4 months
- Day & Night Shift




## Main St. to Woodbine Ave. (South Side of the Corridor)

- Backfilling for RW #9, installation of the soakaway and sub ballast will follow, along with final grading (weather permitting)
- Duration: ~ 2 months
- Day & Night Shift

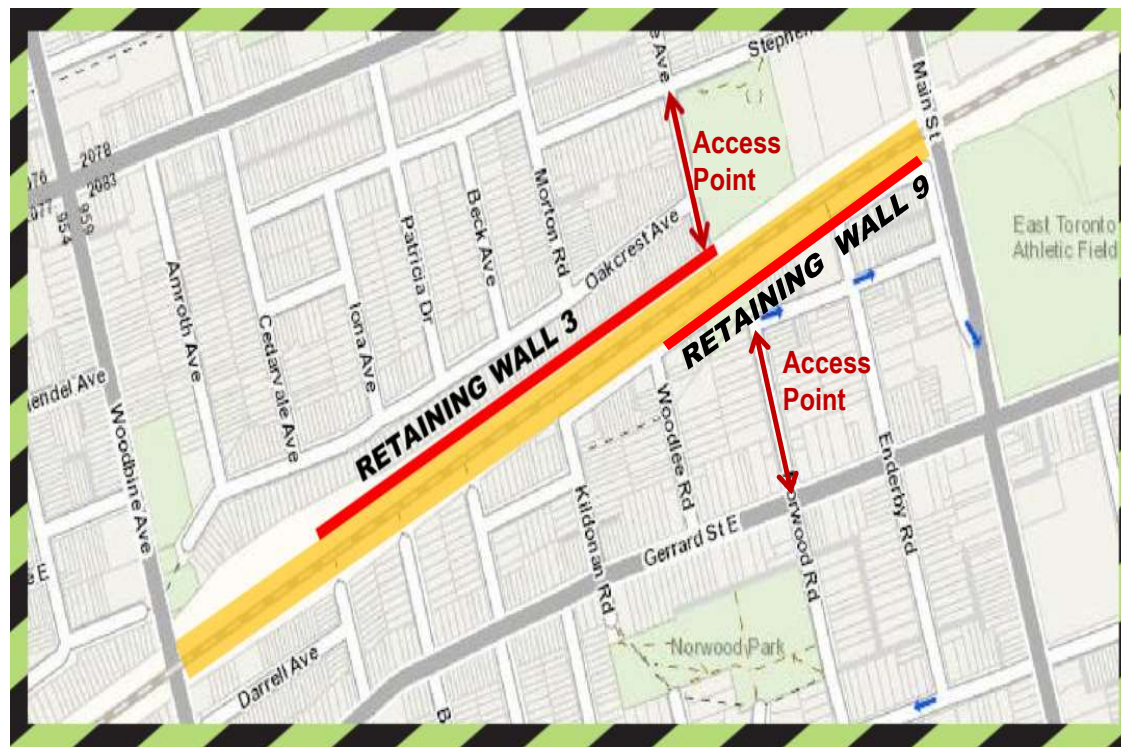

## Warden Bridge Stage 2: Abutment Work


- The installation of temporary shoring is underway on the bridge. This includes piling activities and the installation of tie-backs and lagging
- Road closures are in effect along the west side of Warden Ave. and traffic has been reduced to one lane in each direction
- The pedestrian sidewalk on the west side of the road is now open
- Duration: ~ 4 months
- Day & Night Shift

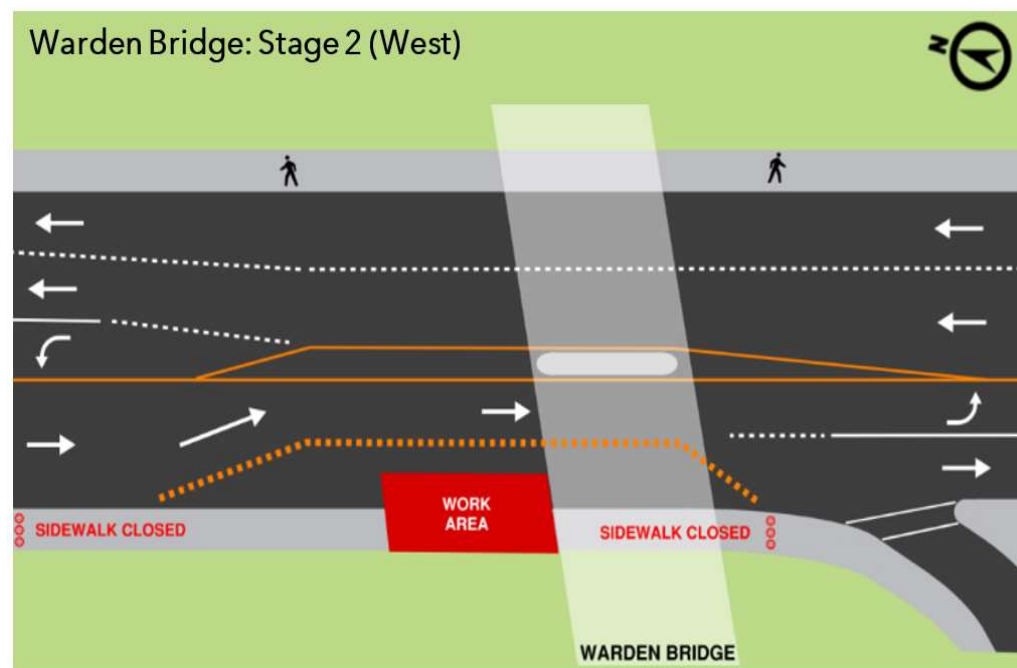

*Note: Traffic plans approved by the City of Toronto*

## Danforth Bridge Stage 2: Abutment Work

- Work is underway on the bridge abutment footings including the installation of temporary shoring, piling, and lagging
- Crews are working on the north and south side of Danforth Ave concurrently and eastbound and westbound traffic has been shifted to the north side of the road.
- The pedestrian underpass on the south side of the road is temporarily closed
- Duration: ~ 6 months
- Day & Night Shift

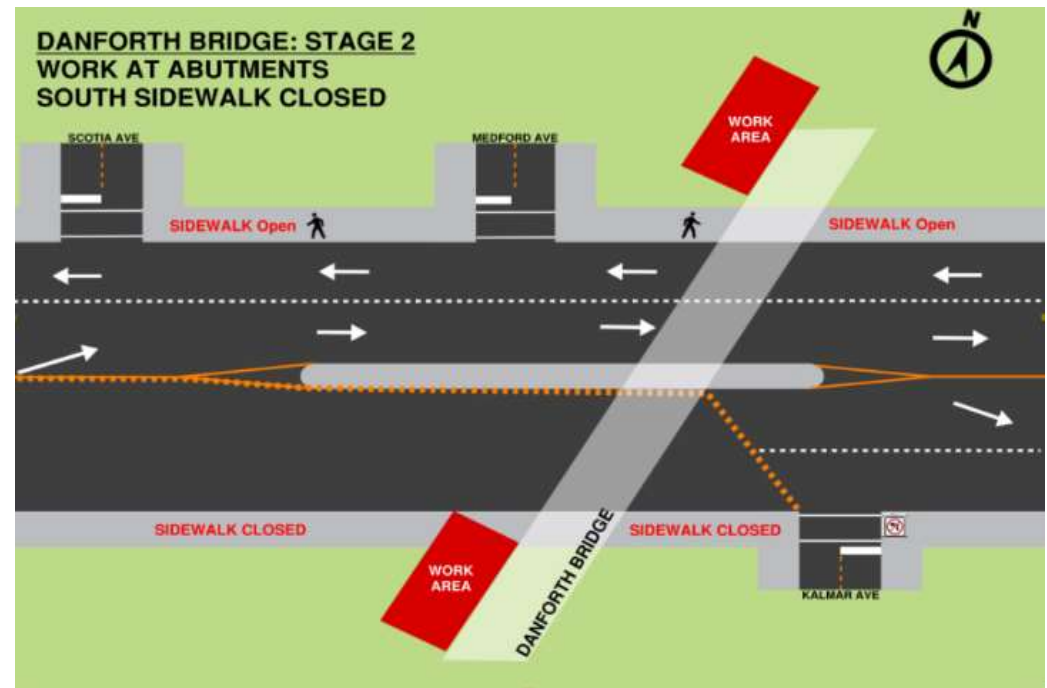


*Note: Traffic plans approved by the City of Toronto*

## Woodbine Bridge Stage 3, Girder Installation

- Crews working in the construction of the bridge deck. This includes the girder installation and required a partial closure over the course of two nights.
- Work took place overnight (completed July 15<sup>th</sup>-16<sup>th</sup>).
- Work on East backwall and approach slabs is ongoing.
- Duration: 2 Nights

*Note: Traffic plans approved by the City of Toronto*

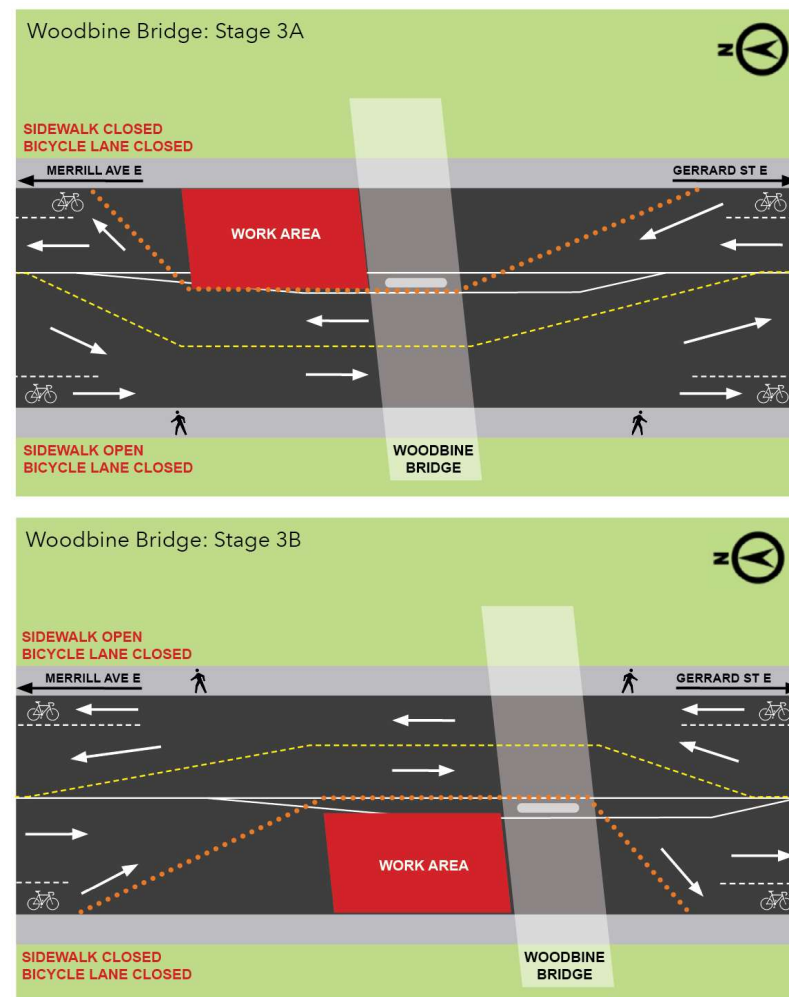

## Slide 17

---

**CW0** Update with details, once the traffic plan is finalized with the COT.  
Charlene Watt, 2023-06-14T15:24:20.966

**CW1** Update photo with applicable details  
Charlene Watt, 2023-06-14T15:24:33.226

# Upcoming Work – Package B

## Woodbine Avenue to Warden Avenue

LS Lakeshore Constructors

July 2023

# Questions & Discussion



