


# Don Yard Rail Corridor

## Bi-Weekly Construction Update

Saturday, November 1, to Saturday, November 15, 2025

This notice provides an update on the work happening in the Don Yard rail corridor over the next two (2) weeks. The notice will be updated on a bi-weekly basis.

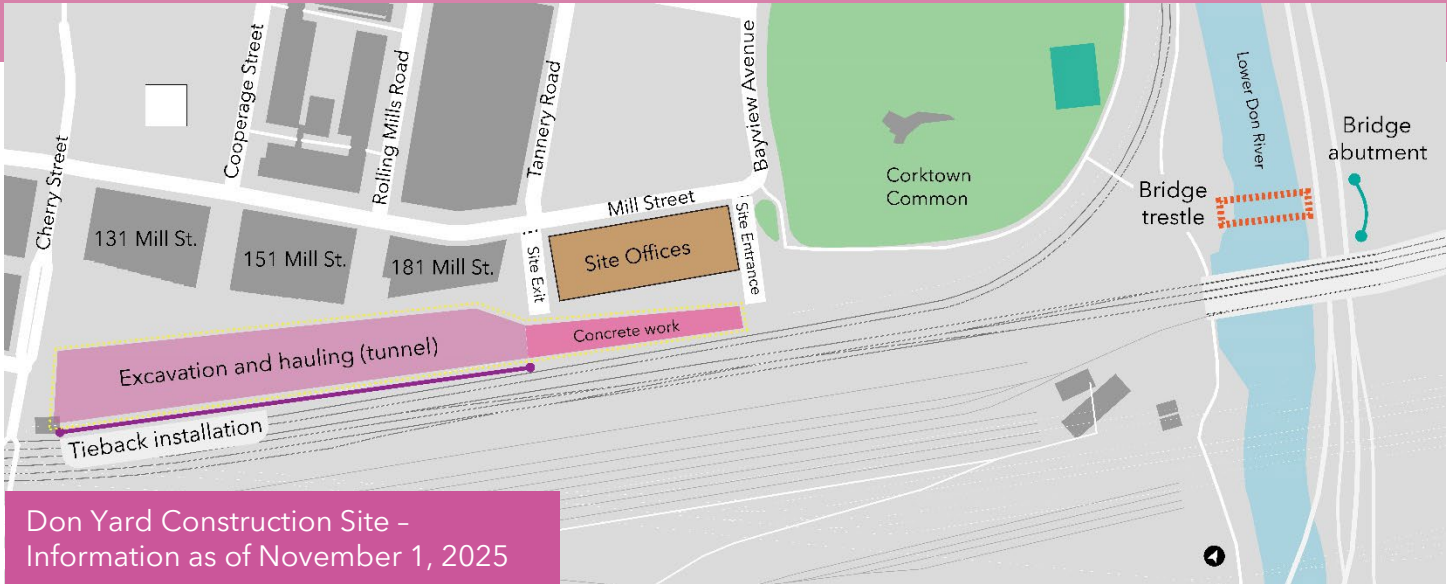

What is happening?

Construction work is underway in the Don Yard rail corridor to prepare for the future Ontario Line. A new subway tunnel and portal are being built in the Don Yard to transition the Ontario Line from underground to surface level. There will also be a new bridge constructed over the Don Valley Parkway. This notice provides a progress update on the works taking place in the Don Yard. **For further details, please carefully review the information provided in the table below.**

| Hours of Work and Duration                                                                                                                                                                                                                                                                                                                                                                                              | Location                                                                                                   | Activity                                                                                                                                                                                                                                                                                            |
|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------------------------------------------------------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| <div><div></div><div><b>Ongoing until December 2025</b><br/><b>Daytime and evenings</b><ul style="list-style-type: none"><li>Monday to Saturday from 7 a.m. – 7 p.m.</li><li><u>Welding continues on weekdays between 3 p.m. – 11 p.m.</u></li><li><u>Intermittent overnight excavation is expected throughout November.</u></li></ul></div></div>                                                                      | <ul style="list-style-type: none"><li>Middle of the site, south of 131, 151, and 181 Mill Street</li></ul> | <b>Excavation, hauling and tieback installation</b><br>Using excavators and dump trucks to remove material (soil) from the site. Using a drill to install steel rods that will support the excavation. Milling and smoothing the piles using an excavator.<br><br>Activities progress west to east. |
| <div><div></div><div><b>Ongoing until December 2025</b><br/><b>Daytime and evenings</b><ul style="list-style-type: none"><li>Monday to Saturday from 7 a.m. – 5 p.m.</li><li><u>Welding work will continue periodically until mid-November on weekday evenings from 3 p.m. – 2 a.m.</u></li></ul></div></div>                                                                                                           | <ul style="list-style-type: none"><li>West of the Don Valley Parkway</li></ul>                             | <b>Bridge trestle work</b><br>Installing the foundations and frame for the temporary bridge trestle. Construction activities include piling, excavation, concrete works, and welding steel beams.                                                                                                   |
| <div><div></div><div><b>Ongoing until January 2026</b><br/><b>Daytime</b><ul style="list-style-type: none"><li>Monday to Friday from 8 a.m. – 6 p.m.</li></ul></div></div>                                                                                                                                                                                                                                              | <ul style="list-style-type: none"><li>At the east end of the site, across the Don River</li></ul>          | <b>Bridge abutment construction</b><br>Loading and removing soil, installing support structures and access stairs, mobilizing a mobile crane and delivering and assembling safety platforms.                                                                                                        |
| <div><div></div><div><b>Ongoing until November 2026</b><br/><b>Daytime</b><ul style="list-style-type: none"><li>Monday to Saturday from 7 a.m. – 7 p.m.</li><li><u>On concrete pour days, shifts may start as early as 2 a.m. Next major pours are scheduled for the morning of Tuesday, November 4, Wednesday, November 5, Thursday, November 13 and Friday, November 14 from 8 a.m.- 1 p.m.</u></li></ul></div></div> | <ul style="list-style-type: none"><li>Within the site east of Tannery Road</li></ul>                       | <b>Permanent Concrete Works</b><br>Waterproofing, rebar installation, forming and concrete pouring for permanent tunnel structure.                                                                                                                                                                  |

\*Work locations may change based on construction progress and site conditions.
