
GO Expansion – Toronto West Construction Email Updates

Monthly Construction Update - Kitchener 4th Track

Date: March 12th, 2026

This is a monthly update on construction activities for the **Kitchener 4th Track** construction project. It includes a summary of work completed in the past month, upcoming or ongoing activities, and any potential community impacts residents and businesses should be aware of.

1. Recently Completed Work

- **Roof Flashing:** Pavilion roofing installation was completed with metal flashing and vertical drainage trough
 - **Architectural Metal Panels:** Composite metal and stone veneer panels were installed on the rear wall of the pavilion.
 - **Pavilion Conduit Works:** Electrical and communications conduits were installed in the pavilion ceiling.
-

2. Upcoming or Ongoing Work

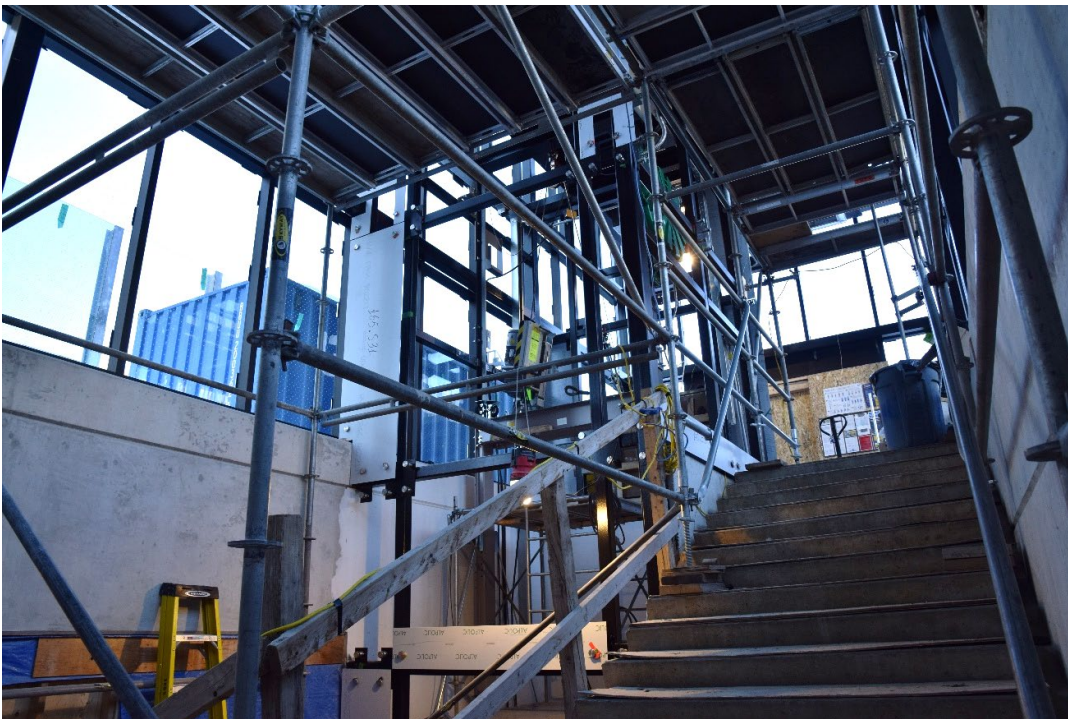


Figure 1: Pavillon elevator location

Activity 1: Elevator Installation

- **Location:** New pedestrian pavilion at the end of Randolph Ave
- **Timing:** Weekdays
- **Potential Impacts:** No significant impacts anticipated
- **Mitigation Measures:** Not Applicable

Why this work is happening now:

The elevator is the last major mechanical system to be installed in the pavilion/tunnel. Once installed, the elevator shaft will be enclosed with glass walls, followed by remaining architectural work in the pavilion.

Activity 2: Track Construction

- **Location:** Rail Corridor between Ernest Ave and Lansdowne Ave
- **Timing:** Weekdays
- **Potential Impacts:** No significant impacts anticipated. Access to Bloor GO station will be maintained at all times.
- **Mitigation Measures:** Not Applicable

Why this work is happening now:

Track work is expected to resume with favourable spring weather on the way. Crews will work to install ballast mats, ballast, and ties, from Ernest Ave to Lansdowne Ave.

3. Looking Ahead

Over the coming months, construction is expected to transition to final finishing works in the pavilion and tunnel, including lighting, architectural features, safety, and security systems. At the same time, the recently installed electrical and mechanical systems will be tested and commissioned. Railpath realignment work (paving, planting, etc.) between Ernest Ave and Bloor St will commence in the spring. We will continue to provide advance notice ahead of any significant changes to construction activity or potential impacts.

Stay Connected

If you have questions or comments about this work, please contact the Toronto West Community Engagement Team:

- **Email:** torontowest@metrolinx.com
- **Phone:** 416-202-6911

Subscribe to our e-newsletter to stay up to date:

- www.metrolinx.com/subscribe

Thank you for your continued patience and interest as construction progresses.
