
Lakeshore East Rail Corridor

Update

# Eglinton GO Station Construction Update

April 2023

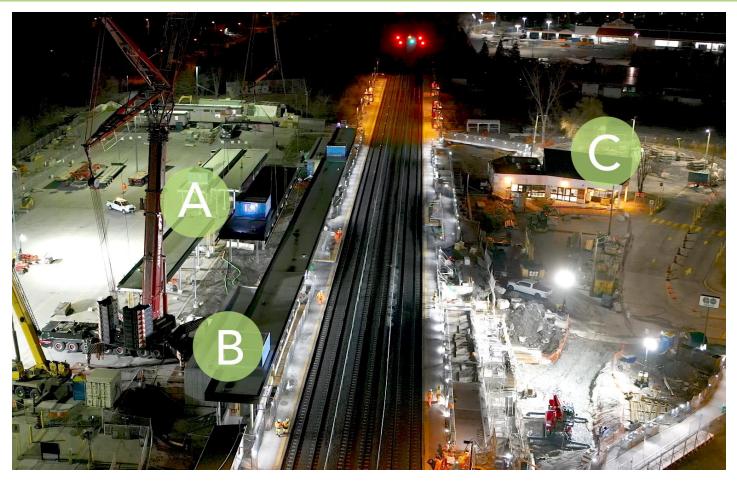

An aerial image showing construction progress on Eglinton GO Station. A) The prefabricated sections of the North Platform about to be hoisted into place; B) The new South Platform; C) Existing Eglinton GO Station Building.

## **Project Overview**

Upgrades at Eglinton GO Station are in the second phase of a two-phase project and will prepare the station to support increased two-way, all-day service in years to come. When the scope of work is completed for the Eglinton GO Accessibility Upgrades project, the station will be fully accessible and will comply with the Accessibility for Ontarians with Disabilities Act, 2005. The project is tracking toward Substantial Completion in May 2024.


Information as of: April 28 2023



# **Construction Update**

Construction work is ongoing at Eglinton GO Station, as crews work to construct the new amenities and improvements around an active rail corridor and transit line. We understand that construction impacts are an inconvenience, and we thank you for your patience as we work to expand and improve the GO network.

The North Platform was recently hoisted into place using an innovative method developed by our contractor - Kenaidan Contracting Ltd. - and used for the first time when the South platform was installed in 2022. By prefabricating the platform in the adjacent parking lot, and hoisting it into place in sections, service impacts were avoided which would have been unavoidable had the new canopy been built on the platform.

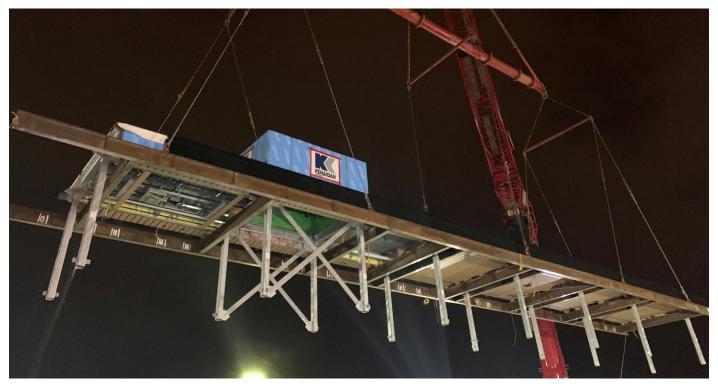

An image of the North Platform being hoisted into place by Kenaidan during the week of March 27.

With the North Platform canopy structure now in place, crews will be working to connect all the sections. Also, the Northwest entrance structure is nearly complete - crews have started on the final concrete stair from tunnel level to platform level.

On the South Platform, crews are currently working on finishing elements of the stair and elevator structures, including exterior finishes by mid-May. The South service rooms are being outfitted with new electrical and communications equipment, including PA, CCTV and lighting. Further, the two new South elevators are scheduled for completion in July.

This notice can be translated into a different language upon request by emailing us at <u>TorontoWest@metrolinx.com</u> Cet avis de travaux de construction est disponible en français sur demande. Si vous êtes intéressé, veuillez envoyer un courriel à <u>TorontoWest@metrolinx.com</u>

#### Contact Us:

- Write to us at: TorontoWest@metrolinx.com
- Find us on Twitter <u>@GOExpansion</u>
- Visit the website: <u>www.metrolinx.com</u>

### **Project Scope**



- Accessible Mini-platforms for level-boarding to the Accessible Coach of GO Trains;
- Two new Pedestrian Tunnels below the tracks connecting the North & South sides of the Station:
- Elevators and stairwells at each entrance to the Pedestrian Tunnels leading up to the platforms;
- Rehabilitation of the North and South Station Platforms including new continuous canopies;
- New trail blazing and wayfinding signage;
- Tactile Walking Surface Indicator (TWSI) installation along platforms edges;
- A new mini-Plaza type entrance to the East tunnel off of Eglinton Ave E;
- Pedestrian accessible ramps with integrated heat-tracing for snow melt on the North side;
- Barrier-free Accessible Parking Spots;
- Reconfiguration of the Passenger Pickup and Drop Off (PUDO) area on the north side;
- Improved landscaping.

This notice can be translated into a different language upon request by emailing us at <u>TorontoWest@metrolinx.com</u>

Cet avis de travaux de construction est disponible en français sur demande. Si vous êtes intéressé, veuillez envoyer un courriel à <u>TorontoWest@metrolinx.com</u>

#### Contact Us:

Write to us at: TorontoWest@metrolinx.com

Find us on Twitter <u>@GOExpansion</u>

Visit the website: <u>www.metrolinx.com</u>
