


# Lakeshore East Rail Corridor: Weekly In-Corridor Work Update

Update for the weeks of: Sunday, September 1 - Sunday, September 15, 2024

Hours of work: Work is not expected to take place on Labour Day (Mon, Sep 2)

- Daytime: Monday- Friday, with periodic weekend work, from 7 a.m.- 7 p.m.
- Overnight: Monday - Sunday from 8 p.m.- 5 a.m. (nights of work depend on activity - further details below).

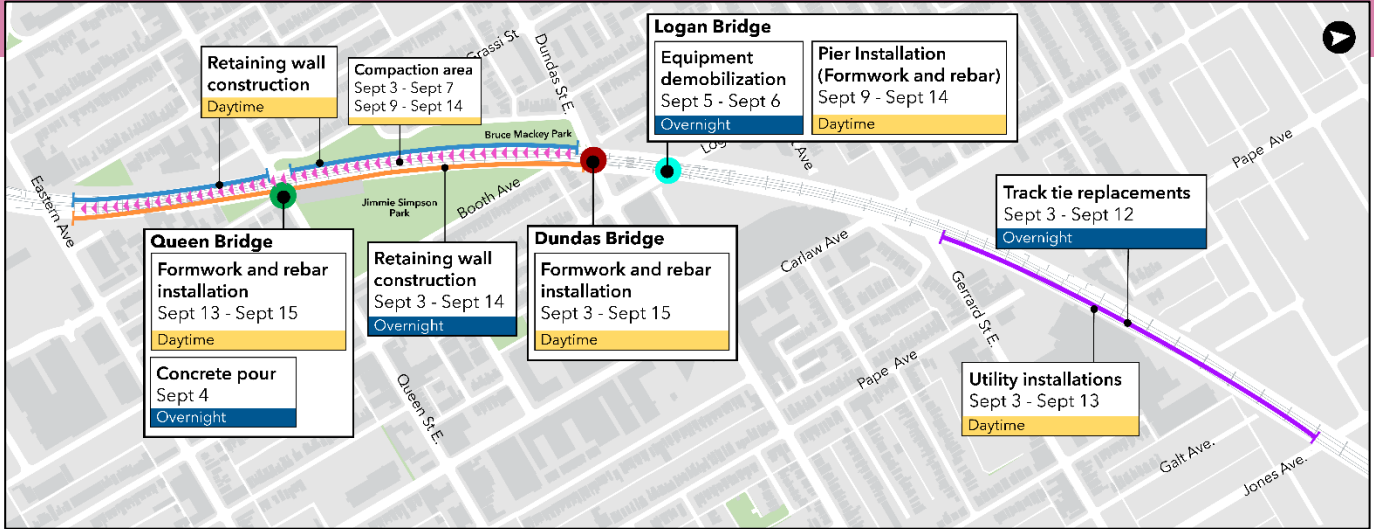




This notice provides an update on the work happening in the rail corridor over the next two (2) weeks. It is updated every Friday.

### What is happening?

Construction work is underway in the Lakeshore East rail corridor to prepare for the future Ontario Line. This notice provides a progress update on the works taking place in the rail corridor. **Certain construction activities may cause noise and vibration at nearby properties. For further details, please carefully review the information provided in the table below.**

| Overnight Work (Monday - Sundays, 8 p.m.- 5 a.m.)     |  |  |
|---|--|--|
| Date  | Location   | Activity   |
| Tuesday, September 3, - Thursday, September 12, 2024  | Within the rail corridor between Gerrard St. E. and Jones Ave. | <b>Track tie replacements.</b><br>• Track tie replacements take place Sun - Thurs            |
| Tuesday, September 3 - Saturday, September 14, 2024   | Within the rail corridor between Eastern Ave. and Dundas St E. | <b>Retaining wall construction</b><br>Retaining wall work takes place periodically Mon - Sat |
| Wednesday September 4, 2024                           | Queen bridge   | <b>Concrete pour</b><br>Starting at 2 a.m. for approximately ten hours                       |
| Thursday September 5, 2024 & Friday September 6, 2024 | Logan bridge   | <b>Equipment demobilization</b><br>Starting at 4 a.m. for approximately 4 hours              |

| Daytime Work (Monday - Saturdays, 7 a.m.- 7 p.m.)     |               |  |
|---|---------------|--|
| Date  | Location      | Activity   |
| Tuesday September 3, 2024 - Sunday September 15, 2024 | Queen bridge  | <b>Formwork and Rebar Installation</b><br>From 7 a.m. - 5 p.m. Saturday and Sunday |
| Tuesday September 3, 2024 - Sunday September 15, 2024 | Dundas bridge | <b>Formwork and Rebar Installation</b><br>From 7 a.m. - 5 p.m. Saturday and Sunday |
| Tuesday September 3, 2024 - Friday September 13, 2024 | Logan bridge  | <b>Caisson Installation</b><br>From 7 a.m. - 5 p.m. incl. Saturday                 |

|  |  |   |
|--|--|---|
|  Monday September 9, 2024 - Saturday September 14, 2024 | Logan bridge   | <b>Pier Installation (Formwork and Rebar)</b><br>From 7 a.m. - 5 p.m. incl. Saturday  |
|  Tuesday, September 3 to Saturday, September 14, 2024   | Within rail corridor, between Eastern Ave- Queen St E and Queen St E to Dundas St E. | <b>Retaining wall construction</b><br>Residents in nearby properties may feel vibrations during compaction work; noise and vibration monitoring is in place to ensure regulatory limits are maintained.<br><b>Approx. dates for compaction work</b><br><b>Tues, Sep 3 - Sat, Sep 7:</b> Periodic compaction work will be ongoing in the rail corridor between Eastern Ave and Dundas St. E.<br><b>Mon, Sep 9 - Sat, Sep 14:</b> Periodic compaction work will be ongoing in the rail corridor between Eastern Ave and Dundas St. E. |
|  Tuesday, September 3 - Friday September 13, 2024       | Within the rail corridor between Gerrard St. E. and Jones Ave.                       | <b>Utility Installations</b><br><ul style="list-style-type: none"> <li>Utility installations take place Mon-Fri</li> </ul>  |

### What to Expect

- Overnight work is required to complete activities that construction crews cannot do safely while trains are active and running in the corridor.
- Excavators, trucks, compactors, loaders, skid steers, and mobile cranes will be used to complete daytime work activities.
- Residents in nearby properties may experience vibration from the work; monitoring is in place to ensure levels stay within acceptable limits.
- Various mitigation measures will be implemented to reduce disruption.
- Overnight site lighting will be positioned downward into the rail corridor and away from residential properties.
- Construction equipment and materials will be secured within the work zones.
- Work may be rescheduled due to inclement weather and/or unforeseen circumstances.
- Work locations are subject to change and may vary based on site conditions and/or schedule requirements.

### About the project

- 15.6-kilometre subway line that will make it faster and easier to travel within Toronto and beyond.
- 15 stops and more than 40 connections to other transit, including GO train, subway, LRT, streetcar and bus lines.
- Approximately 30 minutes from one end of the line to the other.
- 28,000 fewer cars on the road each day.

#### Contact us:

Call us 24/7 at: [416-202-5100](tel:416-202-5100)  
Write to us at: [ontarioline@metrolinx.com](mailto:ontarioline@metrolinx.com)  
Find us on Twitter, Facebook, and Instagram: [@ontarioline](https://www.instagram.com/ontarioline)  
Visit the website: [www.metrolinx.com/ontarioline](http://www.metrolinx.com/ontarioline)

#### Visit our community offices:

**770 Queen Street East (near Queen & Broadview)**  
General hours:  
Mondays, Tuesdays, and Fridays: 9:00 a.m. to 5:00 p.m.  
Wednesdays and Thursdays: 10:00 a.m. to 6:00 p.m.

#### Thorncliffe Park:

East York Town Centre  
45 Overlea Blvd., Toronto, ON M4H 1C3  
Unit 153 (across from the Rogers store)  
General hours:  
Monday - Friday, 9 a.m. - 5 p.m.
