


Lakeshore East Rail Corridor: Weekly In-Corridor Work Update

Update for the weeks of: Sunday, September 15 - Sunday, September 29, 2024

Hours of work:

- Daytime: Monday- Friday, with periodic weekend work, from 7 a.m.- 7 p.m.
- Overnight: Monday - Sunday from 8 p.m.- 5 a.m. (nights of work depend on activity - further details below).

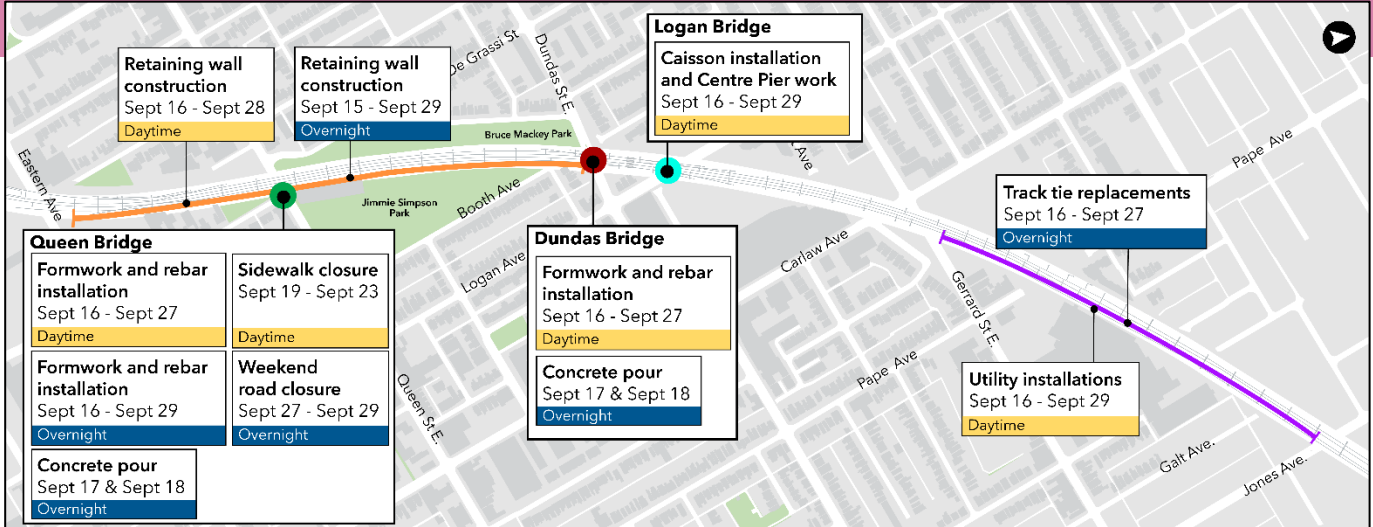







This notice provides an update on the work happening in the rail corridor over the next two (2) weeks. It is updated every Friday.

What is happening?

Construction work is underway in the Lakeshore East rail corridor to prepare for the future Ontario Line. This notice provides a progress update on the works taking place in the rail corridor. **Certain construction activities may cause noise and vibration at nearby properties. For further details, please carefully review the information provided in the table below.**

Overnight Work (Monday - Sundays, 8 p.m.- 5 a.m.)		
Date	Location	Activity
Monday September 16 - Friday, September 27, 2024	Within the rail corridor between Gerrard St. E. and Jones Ave.	Track tie replacements. • Track tie replacements take place Monday to Friday
Sunday, September 15 - Sunday, September 29, 2024	Within the rail corridor between Eastern Ave. and Dundas St E.	Retaining wall construction Retaining wall work takes place periodically Mon - Sun Approx. dates for retaining wall construction. Mon, Sept 16 - Tues, Sept 17: Periodic work will be ongoing in the rail corridor around the Booth Ave and Paisley Ave area. Wed, Sept 18 - Sun, Sept 22: Periodic work will ongoing in the rail corridor between Queen St E and Eastern Ave. Mon, Sept 23 - Sun, Sept 29: Periodic work will ongoing in the rail corridor between Queen St E and Eastern Ave.
Tuesday September 17, 2024 Thursday, September 19, 2024	Queen bridge Dundas bridge	Concrete pour Starting at 9 p.m. for approximately ten hours.
Monday September 16 - Sunday, September 29, 2024	Queen bridge	Formwork and Rebar Installations Periodically overnight between 8 p.m. - 5 a.m.
Friday September 27 - Sunday September 29, 2024	Queen Street East	Weekend Road Closure for Bridge Girder Installation

Daytime Work (Monday - Saturdays, 7 a.m.- 7 p.m.)

Date	Location	Activity
 Thursday September 19 - Monday September 23, 2024	Queen Street East	Sidewalk Closure
 Monday September 16 - Friday, September 27, 2024 	Dundas and Queen bridges	Formwork and Rebar Installation From 7 a.m. - 5 p.m. Saturday and Sunday
 Monday September 16 - Sunday, September 29, 2024	Logan bridge	Caisson Installation and Centre Pier Work
 Monday, September 16 - Saturday, September 28, 2024	Within rail corridor, between Eastern Ave- Queen St E and Queen St E to Dundas St E.	Retaining wall construction Residents in nearby properties may feel vibrations during compaction work; noise and vibration monitoring is in place to ensure regulatory limits are maintained. Approx. dates for compaction work Mon, Sept 16 - Tues, Sept 17: Periodic compaction work will be ongoing in the rail corridor around the Booth Ave and Paisley Ave area. Wed, Sept 18 - Sat, Sept 21: Periodic compaction work will be ongoing in the rail corridor between Queen St E and Eastern Ave. Mon, Sept 23 - Sat, Sept 28: Periodic compaction work will be ongoing in the rail corridor between Queen St E and Eastern Ave.
 Monday September 16 - Sunday, September 29, 2024	Within the rail corridor between Gerrard St. E. and Jones Ave.	Utility Installations <ul style="list-style-type: none"> • Utility installations take place Mon-Fri

What to Expect

- Overnight work is required to complete activities that construction crews cannot do safely while trains are active and running in the corridor.
- Excavators, trucks, compactors, loaders, skid steers, and mobile cranes will be used to complete daytime work activities.
- Residents in nearby properties may experience vibration from the work; monitoring is in place to ensure levels stay within acceptable limits.
- Various mitigation measures will be implanted to reduce disruption.
- Overnight site lighting will be positioned downward into the rail corridor and away from residential properties.
- Construction equipment and materials will be secured within the work zones.
- Work may be rescheduled due to inclement weather and/or unforeseen circumstances.
- Work locations are subject to change and may vary based on site conditions and/or schedule requirements.

About the project

- 15.6-kilometre subway line that will make it faster and easier to travel within Toronto and beyond.
- 15 stops and more than 40 connections to other transit, including GO train, subway, LRT, streetcar and bus lines.
- Approximately 30 minutes from one end of the line to the other.
- 28,000 fewer cars on the road each day.

Contact us:

Call us 24/7 at: [416-202-5100](tel:416-202-5100)
 Write to us at: ontarioline@metrolinx.com
 Find us on Twitter, Facebook, and Instagram: [@ontarioline](https://www.instagram.com/ontarioline)
 Visit the website: www.metrolinx.com/ontarioline

Visit our community offices:

770 Queen Street East (near Queen & Broadview)
 General hours:
 Mondays, Tuesdays, and Fridays: 9:00 a.m. to 5:00 p.m.
 Wednesdays and Thursdays: 10:00 a.m. to 6:00 p.m.

Thorncliffe Park:

East York Town Centre
 45 Overlea Blvd., Toronto, ON M4H 1C3
 Unit 153 (across from the Rogers store)
 General hours:
 Monday - Friday, 9 a.m. - 5 p.m.
