


Lakeshore East Rail Corridor: Weekly In-Corridor Work Update

Update for the weeks of: Saturday, February 1 to Saturday, February 15, 2025

Hours of work:

- Daytime: Monday- Friday, with occasional weekend work, from 7 a.m.- 7 p.m.
- Overnight: Monday - Sunday from 8 p.m.- 5 a.m. (nights of work depend on activity - further details below).

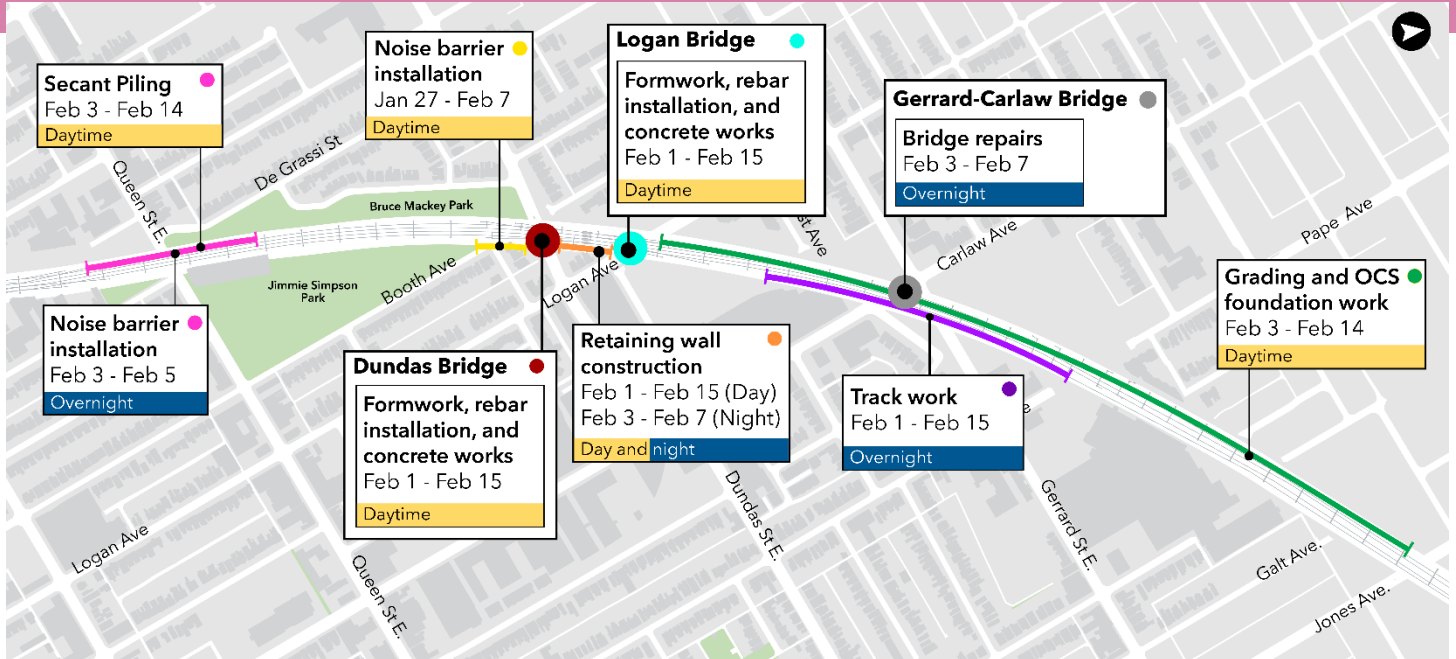







This notice provides an update on the work happening in the rail corridor over the next two (2) weeks. It is updated every Friday.

What is happening?

Construction work is underway in the Lakeshore East rail corridor to prepare for the future Ontario Line. This notice provides a progress update on the works taking place in the rail corridor. **Certain construction activities may cause noise and vibration at nearby properties. For further details, please carefully review the information provided in the table below.**

Overnight Work (Monday - Sundays, 8 p.m. - 5 a.m.)		
Date	Location	Activity
<p>● Saturday February 1 - Saturday February 15, 2025 (weekdays and weekends)</p>	<p>Within the rail corridor between Thackeray St. and Pape Ave.</p>	<p>Track work Removing tracks and constructing a track crossing at Pape Avenue.</p>
<p>● Monday February 3 - Friday February 7, 2025 (weekdays)</p>	<p>Gerrard St. and Carlaw Ave. bridge</p>	<p>Bridge repairs Excavation and material removals to repair the bridge deck</p>
<p>● Monday February 3 - Friday February 7, 2025 (weekdays)</p>	<p>Within the rail corridor between Dundas and Logan bridge</p>	<p>Retaining Wall Work Stockpiling and laying material using a loader, trucks, and small hand tools. No compaction work will take place at night.</p>
<p>● Monday February 3 - Wednesday February 5, 2025</p>	<p>Within the rail corridor east and west of Queen Street</p>	<p>Noise Barrier Installation Installing temporary noise barriers at the top of the rail corridor. Installation will be between 7 p.m. - 5 a.m.</p>

Daytime/Evening Work Monday- Friday, with some weekend work as noted below, from 7 a.m. - 7 p.m.		
Date	Location	Activity
 Saturday February 1 - Saturday February 15, 2025 (weekdays and weekends) 	Dundas and Logan bridges	Formwork, rebar installation, and concrete works Sat Feb 1 to Sun Feb 2: Logan bridge rebar installation
 Monday January 27 - Friday, February 7, 2025 (weekdays)	Booth Ave. and Paisley Ave.	Noise barrier installation Drilling footings for noise wall posts *Sidewalk closure at the north-west corner of Booth-Paisley will be in place starting Wed Feb 5 for approx. three weeks to complete retaining wall work. *Residents in nearby properties may feel vibrations during compaction work; noise and vibration monitoring is in place to ensure regulatory limits are maintained.
 Monday February 3 - Friday February 14, 2025 (weekdays)	Within the rail corridor between Logan Ave. and Jones Ave.	Grading work and OCS foundation work Leveling and laying track ballast and granular material. Installing foundations for OCS poles.
 Monday February 3 - Friday February 14, 2025 (weekdays)	Within the rail corridor north and south of the Queen Street bridge	Secant Piling at Queen bridge Drilling piles for the future Riverside-Leslieville Station. A drill rig will be used to complete this work.
 Saturday February 1 - Saturday February 15, 2025 (weekdays and weekends)	Within the rail corridor between Dundas and Logan bridges	Retaining wall construction Placing concrete blocks (T-walls), backfilling and compacting granular material *Residents in nearby properties may feel vibrations during compaction work; noise and vibration monitoring is in place to ensure regulatory limits are maintained.

What to Expect

- Overnight work is required to complete activities that construction crews cannot do safely while trains are active and running in the corridor.
- Excavators, trucks, compactors, loaders, skid steers, and mobile cranes will be used to complete daytime work activities.
- Residents in nearby properties may experience noise and vibration from the work; monitoring is in place to ensure levels stay within acceptable limits.
- Various mitigation measures will be implanted to reduce disruption.
- Overnight site lighting will be positioned downward into the rail corridor and away from residential properties.
- Construction equipment and materials will be secured within the work zones.
- Work may be rescheduled due to inclement weather and/or unforeseen circumstances.
- Work locations are subject to change and may vary based on site conditions and/or schedule requirements.

About the project

- 15.6-kilometre subway line that will make it faster and easier to travel within Toronto and beyond.
- 15 stops and more than 40 connections to other transit, including GO train, subway, LRT, streetcar and bus lines.
- Approximately 30 minutes from one end of the line to the other.

Contact us:

Call us 24/7 at: [416-202-5100](tel:416-202-5100)
 Write to us at: ontarioline@metrolinx.com
 Find us on Twitter, Facebook, and Instagram: [@ontarioline](https://www.instagram.com/ontarioline)
 Visit the website:
www.metrolinx.com/ontarioline

Visit our community offices:

770 Queen Street East (near Queen & Broadview)
 General hours:
 Mondays, Tuesdays, and Fridays: 9:00 a.m. to 5:00 p.m.
 Wednesdays: 1:00 p.m. to 6:00 p.m.
 Thursdays: 10:00 a.m. to 6:00 p.m.

Thorncliffe Park:

East York Town Centre
 45 Overlea Blvd., Toronto, ON M4H 1C3
 Unit 153 (across from the Rogers store)
 General hours:
 Monday - Friday, 9 a.m. - 5 p.m.
